



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

Insured: Cross Hill

Estimator: Damian Reyes
Company: Valcon Contracting Corp.

Business: (718) 652-0190 x 106
E-mail: damian@valconcontractingcorp.com

Claim Number:

Policy Number:

Type of Loss:

Date of Loss: 9/2/2021 11:49 PM Date Received:
Date Inspected: Date Entered: 11/8/2021 11:48 AM

Price List: NYWP8X_SEP21
Restoration/Service/Remodel
Estimate: CROSS_HILL

This loss was cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning

See page 68 for total "Dwelling Loss" of
\$235,195.60.
The stated amount fully reimbursed by YPS
insurance carrier Travelers.



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CROSS_HILL

CROSS_HILL

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
1. Dumpster load - Approx. 40 yards, 7-8 tons of debris	2.00 EA	1,204.00	0.00	0.00	2,408.00
2. Dumpster load - Approx. 30 yards, 5-7 tons of debris	3.00 EA	1,072.00	0.00	0.00	3,216.00
3. Single axle dump truck - per load - including dump fees	1.00 EA	406.24	0.00	0.00	406.24
4. Haul debris - per pickup truck load - including dump fees	3.00 EA	215.07	0.00	0.00	645.21
5. Commercial Supervision / Project Management - per hour	103.00 HR	0.00	91.72	0.00	9,447.16
1 supervisor on the following days for 7 hours day 1 and 8 hours each after (9/4, 9/5, 9/6, 9/7, 9/8, 10/2, 10/3, 10/4, 10/5, 10/6, 10/7, 10/8 & 10/11)					
6. Negative air fan/Air scrubber (24 hr period) - No monit.	120.00 DA	0.00	71.37	0.00	8,564.40
Initial Set up 12 machines for 10 days					
7. Add for HEPA filter (for negative air exhaust fan)	20.00 EA	0.00	195.55	0.00	3,911.00
8. Neg. air fan/Air scrub.-XLrg (per 24 hr period)-No monit.	35.00 DA	0.00	156.37	0.00	5,472.95
Used on the second trip to clean up 5 xlarge machines for 7 days					
9. Add for HEPA filter (for neg. air machine/vacuum - Large)	10.00 EA	0.00	301.55	0.00	3,015.50
10. Equipment setup, take down, and monitoring (hourly charge)	8.00 HR	0.00	60.41	0.00	483.28
Set up and take down 2 times					
11. Equipment decontamination charge - per piece of equipment	17.00 EA	0.00	51.10	0.00	868.70
12. Clean cove base molding - rubber or vinyl	LF	0.00	0.38	0.00	0.00
13. Discounts (Bid Item)	1.00 EA	0.00	-2,477.87	0.00	-2,477.87
adjustment to match carrier's estimate					
Total: CROSS_HILL				0.00	35,960.57

Basement


Basement

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
14. Clean cove base molding - rubber or vinyl	LF	0.00	0.38	0.00	0.00
Total: Basement				0.00	0.00



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

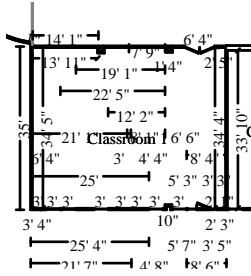

Classroom 1

Height: 13' 5"

1,952.58 SF Walls	1,421.90 SF Ceiling
3,374.48 SF Walls & Ceiling	1,421.90 SF Floor
157.99 SY Flooring	148.22 LF Floor Perimeter
157.55 LF Ceil. Perimeter	

Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Door	3' X 6' 8"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Door	6' 4" X 6' 8"	Opens into HALLWAY

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
15. Remove Suspended ceiling tile - 2' x 4'	1,421.90 SF	0.29	0.00	0.00	412.35
16. Clean the walls - Heavy	1,952.58 SF	0.00	0.50	0.00	976.29
17. Clean the walls	1,952.58 SF	0.00	0.40	0.00	781.03
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
18. Clean light fixture - fluorescent - Heavy	11.00 EA	0.00	22.36	0.00	245.96
19. Clean light fixture - fluorescent	11.00 EA	0.00	15.75	0.00	173.25
20. Additional cost for high wall or ceiling - 11' to 14'	6,635.54 SF	0.00	0.05	0.00	331.78
21. Clean floor - Heavy	1,421.90 SF	0.00	0.66	0.00	938.45
22. Clean floor	1,421.90 SF	0.00	0.46	0.00	654.07
23. Clean window unit (per side) 10 - 20 SF - Heavy	11.00 EA	0.00	23.69	0.00	260.59
24. Clean window unit (per side) 10 - 20 SF	11.00 EA	0.00	16.86	0.00	185.46
25. Clean door - with detail (per side)	3.00 EA	0.00	12.00	0.00	36.00
26. Clean door (per side)	3.00 EA	0.00	8.03	0.00	24.09
27. Clean door hardware - Heavy	3.00 EA	0.00	10.38	0.00	31.14



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190


CONTINUED - Classroom 1

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
28. Clean door hardware	3.00 EA	0.00	7.42	0.00	22.26
29. Clean baseboard - Heavy	148.22 LF	0.00	0.57	0.00	84.49
30. Clean baseboard	148.22 LF	0.00	0.40	0.00	59.29
31. Clean door / window opening (per side)	24.00 EA	0.00	14.53	0.00	348.72
32. Clean door / window opening (per side)	39.33 LF	0.00	0.86	0.00	33.82
33. Cleaning Technician - incl. cleaning agent - per hour	16.00 HR	0.00	47.11	0.00	753.76
2 workers 4 hours each to clean exterior ductwork twice using ladders to reach the high ceiling where they are located. To clean miscellaneous items like exterior of the electrical cut off panels, fire strobe speaker, exit signs ect....					
34. Clean outlet or switch	18.00 EA	0.00	3.88	0.00	69.84
35. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
36. Clean thermostat	2.00 EA	0.00	14.29	0.00	28.58
37. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
38. Clean suspended ceiling grid	1,421.90 SF	0.00	0.34	0.00	483.45
39. Clean cove base molding - rubber or vinyl	148.22 LF	0.00	0.38	0.00	56.32
40. Clean cove base molding - rubber or vinyl	148.22 LF	0.00	0.38	0.00	56.32
Totals: Classroom 1				0.00	7,084.99



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190



Classroom 2 & 2A

Height: 13' 5"

1,672.86 SF Walls	1,168.66 SF Ceiling
2,841.51 SF Walls & Ceiling	1,168.66 SF Floor
129.85 SY Flooring	129.63 LF Floor Perimeter
138.47 LF Ceil. Perimeter	

Door	3' X 6' 8"	Opens into CLASSROOM_2
Door	2' 10" X 6' 8"	Opens into HALLWAY
Door	3' X 6' 8"	Opens into HALLWAY
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
41. Remove Suspended ceiling tile - 2' x 4'	1,168.66 SF	0.29	0.00	0.00	338.91
42. Clean the walls - Heavy	1,672.86 SF	0.00	0.50	0.00	836.43
43. Clean the walls	1,672.86 SF	0.00	0.40	0.00	669.14
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
44. Clean light fixture - fluorescent - Heavy	18.00 EA	0.00	22.36	0.00	402.48
45. Clean light fixture - fluorescent	18.00 EA	0.00	15.75	0.00	283.50
46. Additional cost for high wall or ceiling - 11' to 14'	5,453.73 SF	0.00	0.05	0.00	272.69
47. Clean floor - Heavy	1,168.66 SF	0.00	0.66	0.00	771.32
48. Clean floor	1,168.66 SF	0.00	0.46	0.00	537.58
49. Clean window unit (per side) 10 - 20 SF - Heavy	13.00 EA	0.00	23.69	0.00	307.97
50. Clean window unit (per side) 10 - 20 SF	13.00 EA	0.00	16.86	0.00	219.18



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190


CONTINUED - Classroom 2 & 2A

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
51. Clean door - with detail (per side)	3.00 EA	0.00	12.00	0.00	36.00
52. Clean door (per side)	3.00 EA	0.00	8.03	0.00	24.09
53. Clean door hardware - Heavy	3.00 EA	0.00	10.38	0.00	31.14
54. Clean door hardware	3.00 EA	0.00	7.42	0.00	22.26
55. Clean baseboard - Heavy	129.63 LF	0.00	0.57	0.00	73.89
56. Clean baseboard	129.63 LF	0.00	0.40	0.00	51.85
57. Clean door / window opening (per side)	32.00 EA	0.00	14.53	0.00	464.96
58. Cleaning Technician - incl. cleaning agent - per hour	2.00 HR	0.00	47.11	0.00	94.22
1 worker 2 hours to clean exterior electrical pipe conduit twice. To clean fire strobe speaker and PA speaker					
59. Clean outlet or switch	64.00 EA	0.00	3.88	0.00	248.32
60. Clean phone, TV, or speaker outlet	4.00 EA	0.00	2.96	0.00	11.84
61. Clean thermostat	2.00 EA	0.00	14.29	0.00	28.58
62. Clean sink	1.00 EA	0.00	14.53	0.00	14.53
63. Clean sink - Heavy	1.00 EA	0.00	20.04	0.00	20.04
64. Clean paper dispenser - Heavy	1.00 EA	0.00	10.58	0.00	10.58
65. Clean paper dispenser	1.00 EA	0.00	7.88	0.00	7.88
66. Clean evaporative cooler diffuser	4.00 EA	0.00	17.47	0.00	69.88
67. Clean register - heat / AC	2.00 EA	0.00	6.31	0.00	12.62
68. Clean smoke/carbon monoxide detector	4.00 EA	0.00	7.00	0.00	28.00
69. Clean suspended ceiling grid	1,168.66 SF	0.00	0.34	0.00	397.34
70. Clean cove base molding - rubber or vinyl	129.63 LF	0.00	0.38	0.00	49.26
71. Clean cove base molding - rubber or vinyl	129.63 LF	0.00	0.38	0.00	49.26
Totals: Classroom 2 & 2A				0.00	6,385.74



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190



Classroom 2B

Height: 13' 5"

1,294.57 SF Walls	588.43 SF Ceiling
1,883.00 SF Walls & Ceiling	588.43 SF Floor
65.38 SY Flooring	98.17 LF Floor Perimeter
104.17 LF Ceil. Perimeter	

Door	3' X 6' 8"	Opens into CLASSROOM_4
Door	3' X 6' 8"	Opens into CLASSROOM_2_
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
72. Remove Suspended ceiling tile - 2' x 4'	588.43 SF	0.29	0.00	0.00	170.64
73. Clean the walls - Heavy	1,294.57 SF	0.00	0.50	0.00	647.29
74. Clean the walls	1,294.57 SF	0.00	0.40	0.00	517.83
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
75. Clean light fixture - fluorescent - Heavy	6.00 EA	0.00	22.36	0.00	134.16
76. Clean light fixture - fluorescent	6.00 EA	0.00	15.75	0.00	94.50
77. Additional cost for high wall or ceiling - 11' to 14'	2,746.01 SF	0.00	0.05	0.00	137.30
78. Clean floor - Heavy	588.43 SF	0.00	0.66	0.00	388.36
79. Clean floor	588.43 SF	0.00	0.46	0.00	270.68
80. Clean window unit (per side) 10 - 20 SF - Heavy	7.00 EA	0.00	23.69	0.00	165.83
81. Clean window unit (per side) 10 - 20 SF	7.00 EA	0.00	16.86	0.00	118.02
82. Clean door - with detail (per side)	3.00 EA	0.00	12.00	0.00	36.00
83. Clean door (per side)	3.00 EA	0.00	8.03	0.00	24.09
84. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
85. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
86. Clean baseboard - Heavy	98.17 LF	0.00	0.57	0.00	55.96
87. Clean baseboard	98.17 LF	0.00	0.40	0.00	39.27



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

CONTINUED - Classroom 2B

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
88. Clean door / window opening (per side)	20.00 EA	0.00	14.53	0.00	290.60
89. Cleaning Technician - incl. cleaning agent - per hour 1 worker 2 hours to clean exterior electrical pipe conduit twice. To clean fire strobe speaker and PA speaker	2.00 HR	0.00	47.11	0.00	94.22
90. Clean phone, TV, or speaker outlet	4.00 EA	0.00	2.96	0.00	11.84
91. Clean outlet or switch	40.00 EA	0.00	3.88	0.00	155.20
92. Clean electrical breaker panel - Large	2.00 EA	0.00	19.03	0.00	38.06
93. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
94. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
95. Clean suspended ceiling grid	588.43 SF	0.00	0.34	0.00	200.07
96. Clean cove base molding - rubber or vinyl	98.17 LF	0.00	0.38	0.00	37.30
97. Clean cove base molding - rubber or vinyl	98.17 LF	0.00	0.38	0.00	37.30
Totals: Classroom 2B				0.00	3,731.26




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Classroom 3A

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
111. Clean door hardware	5.00 EA	0.00	7.42	0.00	37.10
112. Clean baseboard - Heavy	65.23 LF	0.00	0.57	0.00	37.18
113. Clean baseboard	65.23 LF	0.00	0.40	0.00	26.09
114. Clean door / window opening (per side)	22.00 EA	0.00	14.53	0.00	319.66
115. Clean door / window opening (per side)	38.33 LF	0.00	0.86	0.00	32.96
116. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker	1.00 HR	0.00	47.11	0.00	47.11
117. Clean phone, TV, or speaker outlet	4.00 EA	0.00	2.96	0.00	11.84
118. Clean outlet or switch	40.00 EA	0.00	3.88	0.00	155.20
119. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
120. Clean suspended ceiling grid	243.61 SF	0.00	0.34	0.00	82.83
121. Clean cove base molding - rubber or vinyl	65.23 LF	0.00	0.38	0.00	24.79
122. Clean cove base molding - rubber or vinyl	65.23 LF	0.00	0.38	0.00	24.79
Totals: Classroom 3A				0.00	2,775.68



Storage Area/Room

Height: 10' 8"

583.39 SF Walls	214.08 SF Ceiling
797.47 SF Walls & Ceiling	214.08 SF Floor
23.79 SY Flooring	52.35 LF Floor Perimeter
58.60 LF Ceil. Perimeter	

Door 3' 3" X 6' 8"
Door 3' X 6' 8"

Opens into HALLWAY
Opens into CLASSROOM_4

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
123. Remove Suspended ceiling tile - 2' x 4'	214.08 SF	0.29	0.00	0.00	62.08
124. Clean the walls - Heavy	583.39 SF	0.00	0.50	0.00	291.70
125. Clean the walls	583.39 SF	0.00	0.40	0.00	233.36
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
126. Clean light fixture - fluorescent - Heavy	2.00 EA	0.00	22.36	0.00	44.72




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Storage Area/Room

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
127. Clean light fixture - fluorescent	2.00 EA	0.00	15.75	0.00	31.50
128. Clean floor - Heavy	214.08 SF	0.00	0.66	0.00	141.29
129. Clean floor	214.08 SF	0.00	0.46	0.00	98.48
130. Clean door - with detail (per side)	2.00 EA	0.00	12.00	0.00	24.00
131. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
132. Clean door hardware - Heavy	2.00 EA	0.00	10.38	0.00	20.76
133. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
134. Clean door / window opening (per side)	4.00 EA	0.00	14.53	0.00	58.12
135. Cleaning Technician - incl. cleaning agent - per hour to clean emergency lights and fire strobe light/speaker	1.00 HR	0.00	47.11	0.00	47.11
136. Clean outlet or switch	4.00 EA	0.00	3.88	0.00	15.52
137. Clean suspended ceiling grid	214.08 SF	0.00	0.34	0.00	72.79
Totals: Storage Area/Room				0.00	1,172.33



Office 3B

Height: 13' 2"

615.92 SF Walls	151.02 SF Ceiling
766.94 SF Walls & Ceiling	151.02 SF Floor
16.78 SY Flooring	47.27 LF Floor Perimeter
49.77 LF Ceil. Perimeter	

Window	2' 10" X 4'	Opens into CLASSROOM_4
Window	2' 10" X 4'	Opens into CLASSROOM_4
Door	2' 6" X 6' 8"	Opens into CLASSROOM_4

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
138. Remove Suspended ceiling tile - 2' x 4'	151.02 SF	0.29	0.00	0.00	43.80
139. Clean the walls - Heavy	615.92 SF	0.00	0.50	0.00	307.96
140. Clean the walls	615.92 SF	0.00	0.40	0.00	246.37
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
141. Clean light fixture - fluorescent - Heavy	2.00 EA	0.00	22.36	0.00	44.72
142. Clean light fixture - fluorescent	2.00 EA	0.00	15.75	0.00	31.50
143. Clean floor - Heavy	151.02 SF	0.00	0.66	0.00	99.67




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Office 3B

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
144. Clean floor	151.02 SF	0.00	0.46	0.00	69.47
145. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
146. Clean door (per side)	1.00 EA	0.00	8.03	0.00	8.03
147. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
148. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
149. Clean door / window opening (per side)	2.00 EA	0.00	14.53	0.00	29.06
150. Cleaning Technician - incl. cleaning agent - per hour to clean emergency lights and fire strobe light/speaker	1.00 HR	0.00	47.11	0.00	47.11
151. Clean outlet or switch	4.00 EA	0.00	3.88	0.00	15.52
152. Clean window unit (per side) 10 - 20 SF - Heavy	2.00 EA	0.00	23.69	0.00	47.38
153. Clean window unit (per side) 10 - 20 SF	2.00 EA	0.00	16.86	0.00	33.72
154. Clean suspended ceiling grid	151.02 SF	0.00	0.34	0.00	51.35
Totals: Office 3B				0.00	1,105.46

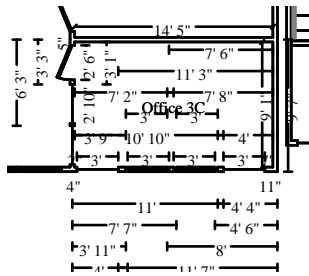

Office 3C

Height: 13' 4"

532.44 SF Walls	130.65 SF Ceiling
663.08 SF Walls & Ceiling	130.65 SF Floor
14.52 SY Flooring	44.43 LF Floor Perimeter
46.93 LF Ceil. Perimeter	

Door	2' 6" X 6' 8"	Opens into CLASSROOM_4
Window	2' 10" X 4'	Opens into CLASSROOM_4
Window	2' 10" X 4'	Opens into CLASSROOM_4
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
155. Remove Suspended ceiling tile - 2' x 4'	130.65 SF	0.29	0.00	0.00	37.89



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190


CONTINUED - Office 3C

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
156. Clean the walls - Heavy	532.44 SF	0.00	0.50	0.00	266.22
157. Clean the walls	532.44 SF	0.00	0.40	0.00	212.98
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
158. Clean light fixture - fluorescent - Heavy	2.00 EA	0.00	22.36	0.00	44.72
159. Clean light fixture - fluorescent	2.00 EA	0.00	15.75	0.00	31.50
160. Clean floor - Heavy	130.65 SF	0.00	0.66	0.00	86.23
161. Clean floor	130.65 SF	0.00	0.46	0.00	60.10
162. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
163. Clean door (per side)	1.00 EA	0.00	8.03	0.00	8.03
164. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
165. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
166. Clean door / window opening (per side)	2.00 EA	0.00	14.53	0.00	29.06
167. Cleaning Technician - incl. cleaning agent - per hour	1.00 HR	0.00	47.11	0.00	47.11
to clean emergency lights and fire strobe light/speaker					
168. Clean outlet or switch	6.00 EA	0.00	3.88	0.00	23.28
169. Clean window unit (per side) 10 - 20 SF - Heavy	9.00 EA	0.00	23.69	0.00	213.21
170. Clean window unit (per side) 10 - 20 SF	9.00 EA	0.00	16.86	0.00	151.74
171. Clean thermostat	2.00 EA	0.00	14.29	0.00	28.58
172. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
173. Clean suspended ceiling grid	130.65 SF	0.00	0.34	0.00	44.42
Totals: Office 3C				0.00	1,349.81



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190



Classroom 4

Height: 13' 3"

1,542.21 SF Walls	1,026.57 SF Ceiling
2,568.78 SF Walls & Ceiling	1,026.57 SF Floor
114.06 SY Flooring	118.15 LF Floor Perimeter
132.90 LF Ceil. Perimeter	

Door	3' X 6' 8"	Opens into STORAGE_4A
Door	3' X 6' 8"	Opens into STOCK_4B
Window	2' 8" X 4'	Opens into OFFICE_4C2
Window	2' 8" X 4'	Opens into OFFICE_4C2
Door	3' X 6' 8"	Opens into OFFICE_4C2
Window	3' X 3'	Opens into Exterior
Window	2' 11 15/16" X 4' 7/16"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' 1/8" X 3' 11 1/2"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	2' 11 13/16" X 4' 3/16"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Door	5' 9" X 6' 8"	Opens into HALLWAY

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
174. Remove Suspended ceiling tile - 2' x 4'	1,026.57 SF	0.29	0.00	0.00	297.71
175. Clean the walls - Heavy	1,542.21 SF	0.00	0.50	0.00	771.11
176. Clean the walls	1,542.21 SF	0.00	0.40	0.00	616.88
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
177. Clean light fixture - fluorescent - Heavy	26.00 EA	0.00	22.36	0.00	581.36
178. Clean light fixture - fluorescent	26.00 EA	0.00	15.75	0.00	409.50
179. Additional cost for high wall or ceiling - 11' to 14'	4,790.67 SF	0.00	0.05	0.00	239.53
180. Clean floor - Heavy	1,026.57 SF	0.00	0.66	0.00	677.54
181. Clean floor	1,026.57 SF	0.00	0.46	0.00	472.22
182. Clean window unit (per side) 10 - 20 SF - Heavy	13.00 EA	0.00	23.69	0.00	307.97
183. Clean window unit (per side) 10 - 20 SF	13.00 EA	0.00	16.86	0.00	219.18
184. Clean door - with detail (per side)	5.00 EA	0.00	12.00	0.00	60.00




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Classroom 4

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
185. Clean door (per side)	5.00 EA	0.00	8.03	0.00	40.15
186. Clean door hardware - Heavy	2.00 EA	0.00	10.38	0.00	20.76
187. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
188. Clean baseboard - Heavy	118.15 LF	0.00	0.57	0.00	67.35
189. Clean baseboard	118.15 LF	0.00	0.40	0.00	47.26
190. Clean door / window opening (per side)	34.00 EA	0.00	14.53	0.00	494.02
191. Clean door / window opening (per side)	38.17 LF	0.00	0.86	0.00	32.83
192. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker and bell	2.00 HR	0.00	47.11	0.00	94.22
193. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
194. Clean outlet or switch	40.00 EA	0.00	3.88	0.00	155.20
195. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
196. Clean thermostat	2.00 EA	0.00	14.29	0.00	28.58
197. Clean register - heat / AC	2.00 EA	0.00	6.31	0.00	12.62
198. Clean electrical breaker panel - Large	4.00 EA	0.00	19.03	0.00	76.12
199. Clean suspended ceiling grid	1,026.57 SF	0.00	0.34	0.00	349.03
200. Clean cove base molding - rubber or vinyl	118.15 LF	0.00	0.38	0.00	44.90
201. Clean cove base molding - rubber or vinyl	118.15 LF	0.00	0.38	0.00	44.90
Totals: Classroom 4				0.00	6,213.46



Stock 4B

Height: 13' 3"

473.73 SF Walls	84.33 SF Ceiling
558.06 SF Walls & Ceiling	84.33 SF Floor
9.37 SY Flooring	34.26 LF Floor Perimeter
37.26 LF Ceil. Perimeter	

Door	3' X 6' 8"	Opens into CLASSROOM_5			
DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
202. Remove Suspended ceiling tile - 2' x 4'	84.33 SF	0.29	0.00	0.00	24.46




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stock 4B

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
203. Clean the walls - Heavy	473.73 SF	0.00	0.50	0.00	236.87
204. Clean the walls	473.73 SF	0.00	0.40	0.00	189.49
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
205. Clean light fixture - Heavy	1.00 EA	0.00	15.96	0.00	15.96
206. Clean light fixture	1.00 EA	0.00	11.85	0.00	11.85
207. Additional cost for high wall or ceiling - 11' to 14'	393.54 SF	0.00	0.05	0.00	19.68
208. Clean floor - Heavy	84.33 SF	0.00	0.66	0.00	55.66
209. Clean floor	84.33 SF	0.00	0.46	0.00	38.79
210. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
211. Clean door (per side)	1.00 EA	0.00	8.03	0.00	8.03
212. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
213. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
214. Clean baseboard - Heavy	34.26 LF	0.00	0.57	0.00	19.53
215. Clean baseboard	34.26 LF	0.00	0.40	0.00	13.70
216. Clean door / window opening (per side)	2.00 EA	0.00	14.53	0.00	29.06
217. Clean outlet or switch	2.00 EA	0.00	3.88	0.00	7.76
218. Clean suspended ceiling grid	84.33 SF	0.00	0.34	0.00	28.67
219. Clean cove base molding - rubber or vinyl	34.26 LF	0.00	0.38	0.00	13.02
220. Clean cove base molding - rubber or vinyl	34.26 LF	0.00	0.38	0.00	13.02
Totals: Stock 4B				0.00	755.35



Storage 4A

Height: 13' 3"

703.40 SF Walls	177.58 SF Ceiling
880.98 SF Walls & Ceiling	177.58 SF Floor
19.73 SY Flooring	51.60 LF Floor Perimeter
54.60 LF Ceil. Perimeter	

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
221. Remove Suspended ceiling tile - 2' x 4'	177.58 SF	0.29	0.00	0.00	51.50



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190


CONTINUED - Storage 4A

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
222. Clean the walls - Heavy	703.40 SF	0.00	0.50	0.00	351.70
223. Clean the walls	703.40 SF	0.00	0.40	0.00	281.36
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
224. Clean light fixture - Heavy	3.00 EA	0.00	15.96	0.00	47.88
225. Clean light fixture	3.00 EA	0.00	11.85	0.00	35.55
226. Additional cost for high wall or ceiling - 11' to 14'	828.69 SF	0.00	0.05	0.00	41.43
227. Clean floor - Heavy	177.58 SF	0.00	0.66	0.00	117.20
228. Clean floor	177.58 SF	0.00	0.46	0.00	81.69
229. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
230. Clean door (per side)	1.00 EA	0.00	8.03	0.00	8.03
231. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
232. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
233. Clean baseboard - Heavy	51.60 LF	0.00	0.57	0.00	29.41
234. Clean baseboard	51.60 LF	0.00	0.40	0.00	20.64
235. Clean door / window opening (per side)	2.00 EA	0.00	14.53	0.00	29.06
236. Clean outlet or switch	4.00 EA	0.00	3.88	0.00	15.52
237. Clean suspended ceiling grid	177.58 SF	0.00	0.34	0.00	60.38
238. Clean cove base molding - rubber or vinyl	51.60 LF	0.00	0.38	0.00	19.61
239. Clean cove base molding - rubber or vinyl	51.60 LF	0.00	0.38	0.00	19.61
Totals: Storage 4A				0.00	1,240.37



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

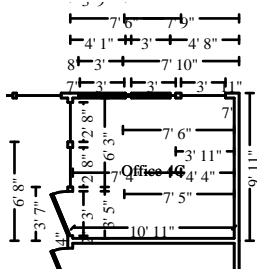

Office 4C

Height: 13' 3"

446.44 SF Walls	102.90 SF Ceiling
549.33 SF Walls & Ceiling	102.90 SF Floor
11.43 SY Flooring	37.68 LF Floor Perimeter
40.68 LF Ceil. Perimeter	

Window	2' 8" X 4'	Opens into CLASSROOM_5
Window	2' 8" X 4'	Opens into CLASSROOM_5
Door	3' X 6' 8"	Opens into CLASSROOM_5
Window	3' X 3'	Opens into Exterior
Window	3' X 4' 3/8"	Opens into Exterior
Window	3' 1/8" X 4' 1/8"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
240. Remove Suspended ceiling tile - 2' x 4'	102.90 SF	0.29	0.00	0.00	29.84
241. Clean the walls - Heavy	446.44 SF	0.00	0.50	0.00	223.22
242. Clean the walls	446.44 SF	0.00	0.40	0.00	178.58
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
243. Clean light fixture - fluorescent - Heavy	2.00 EA	0.00	22.36	0.00	44.72
244. Clean light fixture - fluorescent	2.00 EA	0.00	15.75	0.00	31.50
245. Additional cost for high wall or ceiling - 11' to 14'	480.18 SF	0.00	0.05	0.00	24.01
246. Clean floor - Heavy	102.90 SF	0.00	0.66	0.00	67.91
247. Clean floor	102.90 SF	0.00	0.46	0.00	47.33
248. Clean window unit (per side) 10 - 20 SF - Heavy	7.00 EA	0.00	23.69	0.00	165.83
249. Clean window unit (per side) 10 - 20 SF	7.00 EA	0.00	16.86	0.00	118.02
250. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
251. Clean door (per side)	1.00 EA	0.00	8.03	0.00	8.03
252. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
253. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
254. Clean baseboard - Heavy	37.68 LF	0.00	0.57	0.00	21.48
255. Clean baseboard	37.68 LF	0.00	0.40	0.00	15.07
256. Clean door / window opening (per side)	16.00 EA	0.00	14.53	0.00	232.48




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Office 4C

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
257. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker and fire strobe/speaker	1.00 HR	0.00	47.11	0.00	47.11
258. Clean outlet or switch	10.00 EA	0.00	3.88	0.00	38.80
259. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
260. Clean suspended ceiling grid	102.90 SF	0.00	0.34	0.00	34.99
261. Clean cove base molding - rubber or vinyl	37.68 LF	0.00	0.38	0.00	14.32
262. Clean cove base molding - rubber or vinyl	37.68 LF	0.00	0.38	0.00	14.32
Totals: Office 4C				0.00	1,422.30



Classroom 5

Height: 15' 7"

1,887.63 SF Walls	924.54 SF Ceiling
2,812.17 SF Walls & Ceiling	924.54 SF Floor
102.73 SY Flooring	120.83 LF Floor Perimeter
128.08 LF Ceil. Perimeter	

Door	4' 2" X 6' 8"	Opens into STORAGE_5A
Window	3' X 3'	Opens into Exterior
Window	3' 1/8" X 3' 10 7/8"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' 3/16" X 4' 3/8"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Door	3' 1" X 6' 8"	Opens into HALLWAY

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
263. Remove Suspended ceiling tile - 2' x 4'	924.54 SF	0.29	0.00	0.00	268.12
264. Clean the walls - Heavy	1,887.63 SF	0.00	0.50	0.00	943.82
265. Clean the walls	1,887.63 SF	0.00	0.40	0.00	755.05
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
266. Clean light fixture - fluorescent	21.00 EA	0.00	15.75	0.00	330.75
267. Clean light fixture - fluorescent	21.00 EA	0.00	15.75	0.00	330.75
268. Additional cost for high wall or ceiling - 11' to 14'	4,314.50 SF	0.00	0.05	0.00	215.73



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

CONTINUED - Clasrrom 5

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
269. Clean floor - Heavy	924.54 SF	0.00	0.66	0.00	610.20
270. Clean floor	924.54 SF	0.00	0.46	0.00	425.29
271. Clean window unit (per side) 10 - 20 SF - Heavy	5.00 EA	0.00	23.69	0.00	118.45
272. Clean window unit (per side) 10 - 20 SF	9.00 EA	0.00	16.86	0.00	151.74
273. Clean door - with detail (per side)	3.00 EA	0.00	12.00	0.00	36.00
274. Clean door (per side)	3.00 EA	0.00	8.03	0.00	24.09
275. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
276. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
277. Clean baseboard - Heavy	120.83 LF	0.00	0.57	0.00	68.87
278. Clean baseboard	120.83 LF	0.00	0.40	0.00	48.33
279. Clean door / window opening (per side)	14.00 EA	0.00	14.53	0.00	203.42
280. Clean door / window opening (per side)	32.83 LF	0.00	0.86	0.00	28.23
281. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, and fire strobe/speaker	1.00 HR	0.00	47.11	0.00	47.11
282. Clean phone, TV, or speaker outlet	6.00 EA	0.00	2.96	0.00	17.76
283. Clean outlet or switch	44.00 EA	0.00	3.88	0.00	170.72
284. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
285. Clean suspended ceiling grid	924.54 SF	0.00	0.34	0.00	314.34
286. Clean cove base molding - rubber or vinyl	120.83 LF	0.00	0.38	0.00	45.92
287. Clean cove base molding - rubber or vinyl	120.83 LF	0.00	0.38	0.00	45.92
Totals: Clasrrom 5				0.00	5,253.35




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

Storage 5A

Height: 8' 6"



383.14 SF Walls	109.76 SF Ceiling
492.91 SF Walls & Ceiling	109.76 SF Floor
12.20 SY Flooring	48.41 LF Floor Perimeter
52.58 LF Ceil. Perimeter	

Window	3' X 4'	Opens into Exterior
Window	3' X 4'	Opens into Exterior
Window	3' X 4'	Opens into Exterior
Door	4' 2" X 6' 8"	Opens into CLASRRROM_5

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
288. Remove Suspended ceiling tile - 2' x 4'	109.76 SF	0.29	0.00	0.00	31.83
289. Clean the walls - Heavy	383.14 SF	0.00	0.50	0.00	191.57
290. Clean the walls	383.14 SF	0.00	0.40	0.00	153.26
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
291. Clean floor - Heavy	109.76 SF	0.00	0.66	0.00	72.44
292. Clean floor	109.76 SF	0.00	0.46	0.00	50.49
293. Clean window unit (per side) 10 - 20 SF - Heavy	3.00 EA	0.00	23.69	0.00	71.07
294. Clean window unit (per side) 10 - 20 SF	3.00 EA	0.00	16.86	0.00	50.58
295. Clean door - with detail (per side)	2.00 EA	0.00	12.00	0.00	24.00
296. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
297. Clean door hardware - Heavy	2.00 EA	0.00	10.38	0.00	20.76
298. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
299. Clean baseboard - Heavy	48.41 LF	0.00	0.57	0.00	27.59
300. Clean baseboard	48.41 LF	0.00	0.40	0.00	19.36
301. Clean door / window opening (per side)	6.00 EA	0.00	14.53	0.00	87.18
302. Clean door / window opening (per side)	32.83 LF	0.00	0.86	0.00	28.23
303. Cleaning Technician - incl. cleaning agent - per hour to clean fire strobe/speaker and electrical cut off switches	1.00 HR	0.00	47.11	0.00	47.11
304. Clean outlet or switch	4.00 EA	0.00	3.88	0.00	15.52
305. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
306. Clean suspended ceiling grid	109.76 SF	0.00	0.34	0.00	37.32




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Storage 5A

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
307. Clean cove base molding - rubber or vinyl	48.41 LF	0.00	0.38	0.00	18.40
308. Clean cove base molding - rubber or vinyl	48.41 LF	0.00	0.38	0.00	18.40
Totals: Storage 5A				0.00	1,010.01



Classroom 6

Height: 15' 7"

1,831.88 SF Walls	969.90 SF Ceiling
2,801.78 SF Walls & Ceiling	969.90 SF Floor
107.77 SY Flooring	123.51 LF Floor Perimeter
126.51 LF Ceil. Perimeter	

Door	3' X 6' 8"	Opens into HALLWAY
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' 1/8" X 3' 11 11/16"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 4'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' 7/16" X 3' 10 11/16"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	2' 11 3/4" X 3' 11 1/4"	Opens into Exterior
Window	3' X 3'	Opens into Exterior
Window	3' X 3'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
309. Remove wet suspended ceiling tile and bag for disposal	969.90 SF	0.48	0.00	0.00	465.55
310. Remove Suspended ceiling grid - 2' x 4'	969.90 SF	0.26	0.00	0.00	252.17
311. Tear out wet drywall, cleanup, bag - Cat 3	529.15 SF	1.55	0.00	0.00	820.18
312. Tear out and bag wet insulation - Category 3 water	529.15 SF	1.31	0.00	0.00	693.19
313. Remove Classroom cabinetry - Teacher cabinet - full height	6.00 LF	13.10	0.00	0.00	78.60
314. General Laborer - per hour	2.00 HR	0.00	55.76	0.00	111.52



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Classroom 6

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
2 workers 1 hour each to remove and discard 3 filing cabinets					
315. Seal stud wall for odor control (shellac)	1,831.88 SF	0.00	1.05	0.00	1,923.47
316. Seal floor or ceiling joist system (shellac)	969.90 SF	0.00	1.42	0.00	1,377.26
317. Remove Fluorescent light fixture	22.00 EA	19.68	0.00	0.00	432.96
318. Sink - single bowl - Detach	1.00 EA	0.00	32.23	0.00	32.23
319. General Laborer - per hour	3.00 HR	0.00	55.76	0.00	167.28
To remove burnt plastic and electrical wires that melted into the wall. Worker had to use a grinder to perform this task.					
320. Clean the walls - Heavy	1,831.88 SF	0.00	0.50	0.00	915.94
321. Clean window unit (per side) 10 - 20 SF - Heavy	12.00 EA	0.00	23.69	0.00	284.28
322. Clean door / window opening (per side)	13.00 EA	0.00	14.53	0.00	188.89
323. Clean concrete the floor	969.90 SF	0.00	0.34	0.00	329.77
324. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
325. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
326. General Laborer - per hour	12.00 HR	0.00	55.76	0.00	669.12
to remove 6 6x4 tables and 20 chairs					
327. Neg. air fan/Air scrub.-XLrg (per 24 hr period)-No monit.	39.00 DA	0.00	156.37	0.00	6,098.43
328. Add for HEPA filter (for negative air exhaust fan)	6.00 EA	0.00	195.55	0.00	1,173.30
filter was changed weekly so the AFD can work properly					
329. Ducting - flexible -8" round	100.00 LF	0.00	1.42	0.00	142.00
Used to make the room negative air pressured					
Ducted out the window up to the roof due to students having access to the exterior of that room.					
330. Containment Barrier/Airlock/Decon. Chamber	133.33 SF	0.00	0.95	0.00	126.66
331. Tear out non-salv vinyl, cut & bag - Category 3 water	969.90 SF	2.30	0.00	0.00	2,230.77
332. Remove Vinyl cove - 4" wrap - excludes vinyl material	123.51 LF	2.76	0.00	0.00	340.89
333. Remove Outlet or switch cover	5.00 EA	0.88	0.00	0.00	4.40
334. Clean floor or roof joist system - Heavy	969.90 SF	0.00	1.49	0.00	1,445.15
Totals: Classroom 6				0.00	20,326.39




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Classroom 7

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
354. Clean phone, TV, or speaker outlet	6.00 EA	0.00	2.96	0.00	17.76
355. Clean outlet or switch	42.00 EA	0.00	3.88	0.00	162.96
356. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
357. Clean electrical breaker panel - Large	4.00 EA	0.00	19.03	0.00	76.12
358. Clean suspended ceiling grid	949.48 SF	0.00	0.34	0.00	322.82
359. Clean cove base molding - rubber or vinyl	110.31 LF	0.00	0.38	0.00	41.92
360. Clean cove base molding - rubber or vinyl	110.31 LF	0.00	0.38	0.00	41.92
Totals: Classroom 7				0.00	5,335.66

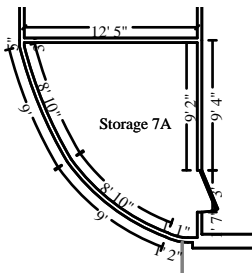

Storage 7A

Height: 10'

444.93 SF Walls	125.77 SF Ceiling
570.70 SF Walls & Ceiling	125.77 SF Floor
13.97 SY Flooring	43.50 LF Floor Perimeter
46.50 LF Ceil. Perimeter	

Door 3' X 6' 8" Opens into CLASSROOM_7

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
361. Clean the walls - Heavy	444.93 SF	0.00	0.50	0.00	222.47
362. Clean the walls	444.93 SF	0.00	0.40	0.00	177.97
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
363. Clean light fixture - fluorescent	2.00 EA	0.00	15.75	0.00	31.50
364. Clean light fixture - fluorescent	2.00 EA	0.00	15.75	0.00	31.50
365. Clean floor - Heavy	125.77 SF	0.00	0.66	0.00	83.01
366. Clean floor	125.77 SF	0.00	0.46	0.00	57.85
367. Clean window unit (per side) 10 - 20 SF - Heavy	2.00 EA	0.00	23.69	0.00	47.38
368. Clean window unit (per side) 10 - 20 SF	2.00 EA	0.00	16.86	0.00	33.72
369. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
370. Clean door (per side)	1.00 EA	0.00	8.03	0.00	8.03
371. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
372. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Storage 7A

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
373. Clean baseboard - Heavy	43.50 LF	0.00	0.57	0.00	24.80
374. Clean baseboard	43.50 LF	0.00	0.40	0.00	17.40
375. Clean door / window opening (per side)	2.00 EA	0.00	14.53	0.00	29.06
376. Cleaning Technician - incl. cleaning agent - per hour to clean fire strobe/speaker and emergency lights	1.00 HR	0.00	47.11	0.00	47.11
377. Clean outlet or switch	6.00 EA	0.00	3.88	0.00	23.28
378. Clean suspended ceiling grid	125.77 SF	0.00	0.34	0.00	42.76
379. Clean cove base molding - rubber or vinyl	43.50 LF	0.00	0.38	0.00	16.53
380. Clean cove base molding - rubber or vinyl	43.50 LF	0.00	0.38	0.00	16.53
Totals: Storage 7A				0.00	940.70



Storage 7B

Height: 10'

401.68 SF Walls	107.62 SF Ceiling
509.30 SF Walls & Ceiling	107.62 SF Floor
11.96 SY Flooring	39.17 LF Floor Perimeter
42.17 LF Ceil. Perimeter	

Door 3' X 6' 8" Opens into CLASSROOM_7

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
381. Clean the walls - Heavy	401.68 SF	0.00	0.50	0.00	200.84
382. Clean the walls	401.68 SF	0.00	0.40	0.00	160.67
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
383. Clean light fixture - fluorescent	1.00 EA	0.00	15.75	0.00	15.75
384. Clean light fixture - fluorescent	1.00 EA	0.00	15.75	0.00	15.75
385. Clean floor - Heavy	107.62 SF	0.00	0.66	0.00	71.03
386. Clean floor	107.62 SF	0.00	0.46	0.00	49.51
387. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
388. Clean door (per side)	1.00 EA	0.00	8.03	0.00	8.03
389. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
390. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
391. Clean baseboard - Heavy	39.17 LF	0.00	0.57	0.00	22.33




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Storage 7B

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
392. Clean baseboard	39.17 LF	0.00	0.40	0.00	15.67
393. Clean door / window opening (per side)	2.00 EA	0.00	14.53	0.00	29.06
394. Clean door / window opening (per side)	LF	0.00	0.86	0.00	0.00
395. Clean outlet or switch	4.00 EA	0.00	3.88	0.00	15.52
396. Clean suspended ceiling grid	107.62 SF	0.00	0.34	0.00	36.59
397. Clean cove base molding - rubber or vinyl	39.17 LF	0.00	0.38	0.00	14.88
398. Clean cove base molding - rubber or vinyl	39.17 LF	0.00	0.38	0.00	14.88
Totals: Storage 7B				0.00	700.31

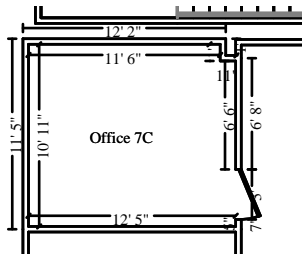

Office 7C

Height: 10'

446.67 SF Walls	134.62 SF Ceiling
581.29 SF Walls & Ceiling	134.62 SF Floor
14.96 SY Flooring	43.67 LF Floor Perimeter
46.67 LF Ceil. Perimeter	

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
399. Remove Suspended ceiling tile - 2' x 4'	134.62 SF	0.29	0.00	0.00	39.04
400. Clean the walls - Heavy	446.67 SF	0.00	0.50	0.00	223.34
401. Clean the walls	446.67 SF	0.00	0.40	0.00	178.67
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
402. Clean light fixture - fluorescent	1.00 EA	0.00	15.75	0.00	15.75
403. Clean light fixture - fluorescent	1.00 EA	0.00	15.75	0.00	15.75
404. Clean floor - Heavy	134.62 SF	0.00	0.66	0.00	88.85
405. Clean floor	134.62 SF	0.00	0.46	0.00	61.93
406. Clean door - with detail (per side)	1.00 EA	0.00	12.00	0.00	12.00
407. Clean door (per side)	1.00 EA	0.00	8.03	0.00	8.03
408. Clean door hardware - Heavy	1.00 EA	0.00	10.38	0.00	10.38
409. Clean door hardware	1.00 EA	0.00	7.42	0.00	7.42
410. Clean baseboard - Heavy	43.67 LF	0.00	0.57	0.00	24.89

Door

3' X 6' 8"

Opens into CLASSROOM_7



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Office 7C

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
411. Clean baseboard	43.67 LF	0.00	0.40	0.00	17.47
412. Clean door / window opening (per side)	2.00 EA	0.00	14.53	0.00	29.06
413. Clean door / window opening (per side)	LF	0.00	0.86	0.00	0.00
414. Clean outlet or switch	4.00 EA	0.00	3.88	0.00	15.52
415. Clean suspended ceiling grid	134.62 SF	0.00	0.34	0.00	45.77
416. Clean cove base molding - rubber or vinyl	43.67 LF	0.00	0.38	0.00	16.59
417. Clean cove base molding - rubber or vinyl	43.67 LF	0.00	0.38	0.00	16.59
Totals: Office 7C				0.00	827.05

Hallway

Height: 10'



2,399.80 SF Walls	1,304.81 SF Ceiling
3,704.61 SF Walls & Ceiling	1,304.81 SF Floor
144.98 SY Flooring	226.54 LF Floor Perimeter
272.96 LF Ceil. Perimeter	


Door	6' 4" X 6' 8"	Opens into CLASSROOM_7
Door	3' X 6' 8"	Opens into CLASSROOM_6
Door	3' 1" X 6' 8"	Opens into CLASRRROM_5
Door	5' 9" X 6' 8"	Opens into CLASSROOM_5
Window	1' 6" X 4'	Opens into STAIRS1
Door	3' 6" X 7'	Opens into STAIRS1
Window	1' 6" X 4'	Opens into STAIRS1
Door	3' 6" X 7'	Opens into STAIRS1
Window	1' 6" X 4'	Opens into STAIRS1
Door	3' 3" X 6' 8"	Opens into STORAGE_AREA
Door	5' 10" X 6' 8"	Opens into CLASSROOM_4
Door	2' 10" X 6' 8"	Opens into CLASSROOM_2_
Door	3' X 6' 8"	Opens into CLASSROOM_2_
Door	6' 4" X 6' 8"	Opens into CLASSROOM_1



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Hallway



Subroom: Room13 (1)

Height: 10'

636.69 SF Walls	334.67 SF Ceiling
971.36 SF Walls & Ceiling	334.67 SF Floor
37.19 SY Flooring	61.62 LF Floor Perimeter
67.78 LF Ceil. Perimeter	

Missing Wall	9' 11 7/8" X 10'	Opens into HALLWAY
Door	6' 2" X 6' 8"	Opens into Exterior
Missing Wall	10' 11" X 10'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
418. Clean the walls - Heavy	3,036.48 SF	0.00	0.50	0.00	1,518.24
419. Clean the walls	3,036.48 SF	0.00	0.40	0.00	1,214.59
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
420. CLEANING	15.00 EA	0.00	0.00	0.00	0.00
421. Clean light fixture - fluorescent	15.00 EA	0.00	15.75	0.00	236.25
422. Clean floor - Heavy	1,639.48 SF	0.00	0.66	0.00	1,082.06
423. Clean floor	1,639.48 SF	0.00	0.46	0.00	754.16
424. Clean door - with detail (per side)	18.00 EA	0.00	12.00	0.00	216.00
425. Clean door (per side)	18.00 EA	0.00	8.03	0.00	144.54
426. Clean door hardware - Heavy	2.00 EA	0.00	10.38	0.00	20.76
427. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
428. Clean baseboard - Heavy	288.16 LF	0.00	0.57	0.00	164.25
429. Clean baseboard	288.16 LF	0.00	0.40	0.00	115.26
430. Clean door / window opening (per side)	22.00 EA	0.00	14.53	0.00	319.66
431. Clean door / window opening (per side)	LF	0.00	0.86	0.00	0.00
432. Cleaning Technician - incl. cleaning agent - per hour	8.00 HR	0.00	47.11	0.00	376.88
to clean water fountain, PA speaker, fire alarm, fire extinguishers, fire pull stations, exit signs, emergency lights and cage, signs and cameras					
433. Clean smoke/carbon monoxide detector	12.00 EA	0.00	7.00	0.00	84.00
434. R&R Stud wall - 2" x 4" x 8' - 24" oc	10.42 LF	2.11	25.59	0.00	288.64
Temp wall for containment. Other side cleaned by school staff for kids can utilize during school hours.					
435. Containment Barrier/Airlock/Decon. Chamber	104.17 SF	0.00	0.95	0.00	98.96
436. Peel & seal zipper	1.00 EA	0.00	13.28	0.00	13.28




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Hallway


DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
437. Clean cove base molding - rubber or vinyl	288.16 LF	0.00	0.38	0.00	109.50
438. Clean cove base molding - rubber or vinyl	288.16 LF	0.00	0.38	0.00	109.50
Totals: Hallway				0.00	6,881.37



Stairs

Height: 27' 5"

313.36 SF Walls	89.83 SF Ceiling
403.19 SF Walls & Ceiling	165.97 SF Floor
18.44 SY Flooring	16.83 LF Floor Perimeter
14.00 LF Ceil. Perimeter	

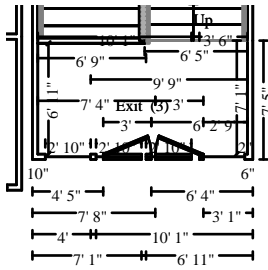

Subroom: Exit (3)

Height: 15'

450.54 SF Walls	91.56 SF Ceiling
542.10 SF Walls & Ceiling	91.56 SF Floor
10.17 SY Flooring	27.75 LF Floor Perimeter
33.75 LF Ceil. Perimeter	


Window	2' 10" X 4' 4"	Opens into Exterior
Door	3' X 6' 8"	Opens into Exterior
Window	2' 10" X 4' 4"	Opens into Exterior
Door	3' X 6' 8"	Opens into Exterior
Window	2' 10" X 4' 4"	Opens into Exterior
Window	2' 10" X 4' 4"	Opens into Exterior
Missing Wall	6' 5" X 15'	Opens into STAIRS



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs




Subroom: Stairs1 (2)

Height: 17' 5"

627.13 SF Walls	149.37 SF Ceiling
776.49 SF Walls & Ceiling	149.37 SF Floor
16.60 SY Flooring	36.00 LF Floor Perimeter
36.00 LF Ceil. Perimeter	

Missing Wall	6' 5" X 17' 4 9/16"	Opens into STAIRS
Window	1' 6" X 4'	Opens into HALLWAY
Door	3' 6" X 7'	Opens into HALLWAY
Window	1' 6" X 4'	Opens into HALLWAY
Door	3' 6" X 7'	Opens into HALLWAY
Window	1' 6" X 4'	Opens into HALLWAY
Missing Wall	6' 4" X 17' 4 9/16"	Opens into STAIRS2



Subroom: Stairs2 (1)

Height: 17' 5"

172.65 SF Walls	87.61 SF Ceiling
260.26 SF Walls & Ceiling	164.76 SF Floor
18.31 SY Flooring	16.54 LF Floor Perimeter
13.83 LF Ceil. Perimeter	

Missing Wall	6' 4" X 17' 4 9/16"	Opens into STAIRS1
---------------------	----------------------------	---------------------------

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
439. Clean the walls - Heavy	1,563.67 SF	0.00	0.50	0.00	781.84
440. Clean the walls	1,563.67 SF	0.00	0.40	0.00	625.47
441. Additional cost for high wall or ceiling - 11' to 14'	1,435.18 SF	0.00	0.05	0.00	71.76
442. Clean balustrade - Heavy	15.42 LF	0.00	4.18	0.00	64.46
443. Clean balustrade	15.42 LF	0.00	2.93	0.00	45.18
444. Clean stair riser - per side - per LF	367.33 LF	0.00	0.62	0.00	227.74
445. Clean stair tread - per side - per LF	342.00 LF	0.00	0.73	0.00	249.66
446. Clean light fixture - fluorescent	4.00 EA	0.00	15.75	0.00	63.00
447. Clean door - with detail (per side)	4.00 EA	0.00	12.00	0.00	48.00
448. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
449. Clean door hardware - Heavy	4.00 EA	0.00	10.38	0.00	41.52
450. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs


DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
451. Clean window unit (per side) 3 - 9 SF - Heavy	6.00 EA	0.00	16.57	0.00	99.42
452. Clean window unit (per side) 3 - 9 SF	6.00 EA	0.00	11.80	0.00	70.80
453. Clean window unit (per side) 10 - 20 SF - Heavy	6.00 EA	0.00	23.69	0.00	142.14
454. Clean window unit (per side) 10 - 20 SF	6.00 EA	0.00	16.86	0.00	101.16
455. Clean handrail - wall mounted - Heavy	46.25 LF	0.00	0.85	0.00	39.31
456. Clean handrail - wall mounted	46.25 LF	0.00	0.58	0.00	26.83
457. Cleaning Technician - incl. cleaning agent - per hour to clean exit signs	1.00 HR	0.00	47.11	0.00	47.11
458. Clean floor - Heavy	240.93 SF	0.00	0.66	0.00	159.01
459. Clean floor	240.93 SF	0.00	0.46	0.00	110.83
Totals: Stairs				0.00	3,077.04



Stairs3

Height: 26' 2"

297.35 SF Walls	83.14 SF Ceiling
380.49 SF Walls & Ceiling	147.61 SF Floor
16.40 SY Flooring	15.92 LF Floor Perimeter
13.67 LF Ceil. Perimeter	



Subroom: Room1 (3)

Height: 13' 5"

401.58 SF Walls	89.96 SF Ceiling
491.54 SF Walls & Ceiling	89.96 SF Floor
10.00 SY Flooring	26.58 LF Floor Perimeter
33.58 LF Ceil. Perimeter	

Missing Wall

6' 1" X 13' 5"

Opens into STAIRS3

Door

3' 6" X 7'

Opens into Exterior

Door

3' 6" X 7'


Opens into Exterior



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs3



Subroom: Stairs5 (1)


Height: 17' 5"

213.80 SF Walls	85.50 SF Ceiling
299.30 SF Walls & Ceiling	160.59 SF Floor
17.84 SY Flooring	22.75 LF Floor Perimeter
19.83 LF Ceil. Perimeter	

Missing Wall

6' 4" X 17' 4 9/16"

Opens into STAIRS4



Subroom: Stairs4 (2)

Height: 17' 5"

505.47 SF Walls	104.12 SF Ceiling
609.59 SF Walls & Ceiling	104.12 SF Floor
11.57 SY Flooring	29.08 LF Floor Perimeter
29.08 LF Ceil. Perimeter	

Missing Wall

6' 1" X 17' 4 9/16"

Opens into STAIRS3

Door

3' 6" X 7'

Opens into Exterior

Door

3' 6" X 7'

Opens into Exterior

Missing Wall

6' 4" X 17' 4 9/16"

Opens into STAIRS5

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
460. Clean the walls - Heavy	1,418.19 SF	0.00	0.50	0.00	709.10
461. Clean the walls	1,418.19 SF	0.00	0.40	0.00	567.28
462. Additional cost for high wall or ceiling - 11' to 14'	1,218.23 SF	0.00	0.05	0.00	60.91
463. Clean balustrade - Heavy	15.42 LF	0.00	4.18	0.00	64.46
464. Clean balustrade	15.42 LF	0.00	2.93	0.00	45.18
465. Clean stair riser - per side - per LF	380.00 LF	0.00	0.62	0.00	235.60
466. Clean stair tread - per side - per LF	354.67 LF	0.00	0.73	0.00	258.91
467. Clean light fixture - fluorescent	4.00 EA	0.00	15.75	0.00	63.00
468. Clean door - with detail (per side)	4.00 EA	0.00	12.00	0.00	48.00
469. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
470. Clean door hardware - Heavy	4.00 EA	0.00	10.38	0.00	41.52
471. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68
472. Clean window unit (per side) 3 - 9 SF - Heavy	6.00 EA	0.00	16.57	0.00	99.42



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

CONTINUED - Stairs3

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
473. Clean window unit (per side) 3 - 9 SF	6.00 EA	0.00	11.80	0.00	70.80
474. Clean window unit (per side) 10 - 20 SF - Heavy	6.00 EA	0.00	23.69	0.00	142.14
475. Clean window unit (per side) 10 - 20 SF	6.00 EA	0.00	16.86	0.00	101.16
476. Clean handrail - wall mounted - Heavy	46.25 LF	0.00	0.85	0.00	39.31
477. Clean handrail - wall mounted	46.25 LF	0.00	0.58	0.00	26.83
478. Cleaning Technician - incl. cleaning agent - per hour to clean exit signs	1.00 HR	0.00	47.11	0.00	47.11
479. Clean floor - Heavy	194.09 SF	0.00	0.66	0.00	128.10
480. Clean floor	194.09 SF	0.00	0.46	0.00	89.28
Totals: Stairs3				0.00	2,899.91
Total: Basement				0.00	80,488.54

Main Level

Main Level

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
481. Clean cove base molding - rubber or vinyl	LF	0.00	0.38	0.00	0.00
Total: Main Level				0.00	0.00




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Hallway

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
484. Cleaning Technician - incl. cleaning agent - per hour 6 workers 8 hours each for 3 days. To clean the 264 lockers inside and outside	288.00 HR	0.00	47.11	0.00	13,567.68
485. Clean light fixture - fluorescent	30.00 EA	0.00	15.75	0.00	472.50
486. Clean floor	3,613.81 SF	0.00	0.46	0.00	1,662.35
487. Clean door (per side)	44.00 EA	0.00	8.03	0.00	353.32
488. Clean door hardware	10.00 EA	0.00	7.42	0.00	74.20
489. Clean baseboard	729.22 LF	0.00	0.40	0.00	291.69
490. Clean door / window opening (per side)	24.00 EA	0.00	14.53	0.00	348.72
491. Clean door / window opening (per side)	73.67 LF	0.00	0.86	0.00	63.36
492. Clean outlet or switch	10.00 EA	0.00	3.88	0.00	38.80
493. Clean smoke/carbon monoxide detector	14.00 EA	0.00	7.00	0.00	98.00
494. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire alarm, fire extinguishers, fire pull stations, exit signs, emergency lights and cage, signs and cameras	8.00 HR	0.00	47.11	0.00	376.88
495. Clean suspended ceiling grid	2,022.12 SF	0.00	0.34	0.00	687.52
Totals: Hallway				0.00	21,166.09



Room 114

Height: 10'

977.07 SF Walls	918.68 SF Ceiling
1,895.75 SF Walls & Ceiling	864.27 SF Floor
96.03 SY Flooring	86.98 LF Floor Perimeter
124.62 LF Ceil. Perimeter	

Window	2' 10" X 7'	Opens into Exterior
Window	2' 10" X 7'	Opens into Exterior
Window	2' 10" X 7'	Opens into Exterior
Window	2' 10" X 7'	Opens into Exterior
Window	2' 10" X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Door	3' 1" X 6' 8"	Opens into HALLWAY



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 114

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
496. Remove Suspended ceiling tile - 2' x 4'	918.68 SF	0.29	0.00	0.00	266.42
497. Clean more than the walls	1,954.14 SF	0.00	0.40	0.00	781.66
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
498. Clean light fixture - fluorescent	50.00 EA	0.00	15.75	0.00	787.50
499. Clean floor	1,728.54 SF	0.00	0.46	0.00	795.13
500. Clean window unit (per side) 10 - 20 SF	16.00 EA	0.00	16.86	0.00	269.76
501. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
502. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
503. Clean baseboard	173.95 LF	0.00	0.40	0.00	69.58
504. Clean door / window opening (per side)	18.00 EA	0.00	14.53	0.00	261.54
505. Cleaning Technician - incl. cleaning agent - per hour	3.00 HR	0.00	47.11	0.00	141.33
to clean PA speaker, fire strobe/speaker, and locker					
506. Clean phone, TV, or speaker outlet	4.00 EA	0.00	2.96	0.00	11.84
507. Clean outlet or switch	20.00 EA	0.00	3.88	0.00	77.60
508. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
509. Clean cabinetry - lower - inside and out	48.17 LF	0.00	16.46	0.00	792.88
510. Clean sink	2.00 EA	0.00	14.53	0.00	29.06
511. Clean sink faucet	2.00 EA	0.00	10.81	0.00	21.62
512. Clean countertop	112.33 SF	0.00	0.82	0.00	92.11
513. Clean cove base molding - rubber or vinyl	173.95 LF	0.00	0.38	0.00	66.10
514. Clean suspended ceiling grid	918.68 SF	0.00	0.34	0.00	312.35
Totals: Room 114				0.00	4,842.32




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 114A

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
528. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
529. Clean radiator cover	2.00 EA	0.00	13.53	0.00	27.06
530. Clean thermostat	2.00 EA	0.00	14.29	0.00	28.58
531. Clean cold air return cover	2.00 EA	0.00	9.73	0.00	19.46
532. Clean cove base molding - rubber or vinyl	257.80 LF	0.00	0.38	0.00	97.96
533. Clean suspended ceiling grid	634.56 SF	0.00	0.34	0.00	215.75
Totals: Room 114A				0.00	3,157.02



Room 113

Height: 10'

1,014.56 SF Walls	1,052.99 SF Ceiling
2,067.55 SF Walls & Ceiling	1,034.84 SF Floor
114.98 SY Flooring	100.86 LF Floor Perimeter
131.90 LF Ceil. Perimeter	

Door	3' X 6' 8"	Opens into STORAGE_ARE2
Door	3' 1" X 6' 8"	Opens into HALLWAY
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
534. Remove Suspended ceiling tile - 2' x 4'	1,052.99 SF	0.29	0.00	0.00	305.37
535. Clean more than the walls	2,029.12 SF	0.00	0.40	0.00	811.65
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
536. Clean light fixture - fluorescent	40.00 EA	0.00	15.75	0.00	630.00
537. Clean floor	2,069.68 SF	0.00	0.46	0.00	952.05
538. Clean window unit (per side) 10 - 20 SF	18.00 EA	0.00	16.86	0.00	303.48




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 113

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
539. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
540. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68
541. Clean baseboard	201.73 LF	0.00	0.40	0.00	80.69
542. Clean door / window opening (per side)	22.00 EA	0.00	14.53	0.00	319.66
543. Cleaning Technician - incl. cleaning agent - per hour	3.00 HR	0.00	47.11	0.00	141.33
to clean PA speaker, fire strobe/speaker, emergency light and alarm sensor					
544. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
545. Clean outlet or switch	40.00 EA	0.00	3.88	0.00	155.20
546. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
547. Clean cabinetry - lower - inside and out	48.33 LF	0.00	16.46	0.00	795.51
548. Clean countertop	48.33 SF	0.00	0.82	0.00	39.63
549. Clean cove base molding - rubber or vinyl	201.73 LF	0.00	0.38	0.00	76.66
550. Clean suspended ceiling grid	1,052.99 SF	0.00	0.34	0.00	358.02
Totals: Room 113				0.00	5,068.73



Storage Area/Room

Height: 10'

414.65 SF Walls	223.17 SF Ceiling
637.82 SF Walls & Ceiling	157.32 SF Floor
17.48 SY Flooring	38.39 LF Floor Perimeter
71.33 LF Ceil. Perimeter	

Door	3' X 6' 8"	Opens into ROOM_112
Window	2' 6" X 3' 6"	Opens into ROOM_112
Door	2' 6" X 6' 8"	Opens into PASSAGE
Door	3' X 6' 8"	Opens into ROOM_113
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
551. Remove Suspended ceiling tile - 2' x 4'	223.17 SF	0.29	0.00	0.00	64.72




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Storage Area/Room

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
552. Clean more than the walls cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning	829.29 SF	0.00	0.40	0.00	331.72
553. Clean light fixture - fluorescent	10.00 EA	0.00	15.75	0.00	157.50
554. Clean floor	314.64 SF	0.00	0.46	0.00	144.73
555. Clean window unit (per side) 10 - 20 SF	6.00 EA	0.00	16.86	0.00	101.16
556. Clean door (per side)	6.00 EA	0.00	8.03	0.00	48.18
557. Clean door hardware	6.00 EA	0.00	7.42	0.00	44.52
558. Clean baseboard	76.77 LF	0.00	0.40	0.00	30.71
559. Clean door / window opening (per side)	12.00 EA	0.00	14.53	0.00	174.36
560. Clean thermostat to clean PA speaker	2.00 EA	0.00	14.29	0.00	28.58
561. Clean register - heat / AC	4.00 EA	0.00	6.31	0.00	25.24
562. Clean outlet or switch	4.00 EA	0.00	3.88	0.00	15.52
563. Clean bookcase	140.67 SF	0.00	1.25	0.00	175.84
564. Clean cabinetry - lower - inside and out	31.00 LF	0.00	16.46	0.00	510.26
565. Clean cabinetry - full height - inside and out	10.00 LF	0.00	28.77	0.00	287.70
566. Clean countertop	62.00 SF	0.00	0.82	0.00	50.84
567. Clean cove base molding - rubber or vinyl	76.77 LF	0.00	0.38	0.00	29.17
Totals: Storage Area/Room				0.00	2,220.75

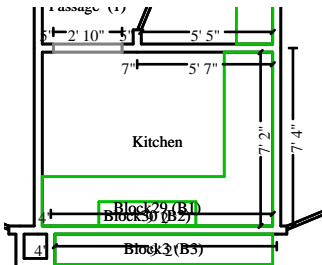

Kitchen

Height: 8'


175.67 SF Walls	68.08 SF Ceiling
243.75 SF Walls & Ceiling	38.48 SF Floor
4.28 SY Flooring	9.80 LF Floor Perimeter
33.33 LF Ceil. Perimeter	



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Kitchen

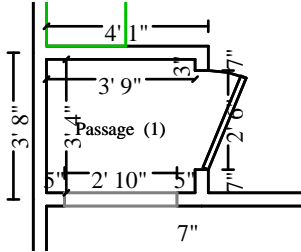

Subroom: Passage (1)

Height: 8'

78.24 SF Walls	12.61 SF Ceiling
90.85 SF Walls & Ceiling	12.61 SF Floor
1.40 SY Flooring	8.89 LF Floor Perimeter
14.22 LF Ceil. Perimeter	

Missing Wall - Goes to Floor

2' 10" X 6' 8"

Opens into KITCHEN

Door

2' 6" X 6' 8"


Opens into STORAGE_ARE2

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
568. Remove Suspended ceiling tile - 2' x 4'	80.69 SF	0.29	0.00	0.00	23.40
569. Clean more than the walls	507.83 SF	0.00	0.40	0.00	203.13
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
570. Clean light fixture - fluorescent	2.00 EA	0.00	15.75	0.00	31.50
571. Clean light fixture	2.00 EA	0.00	11.85	0.00	23.70
572. Clean floor	102.19 SF	0.00	0.46	0.00	47.01
573. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
574. Clean baseboard	37.38 LF	0.00	0.40	0.00	14.95
575. Clean door / window opening (per side)	2.00 EA	0.00	14.53	0.00	29.06
576. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker	1.00 HR	0.00	47.11	0.00	47.11
577. Clean outlet or switch	10.00 EA	0.00	3.88	0.00	38.80
578. Clean smoke/carbon monoxide detector	4.00 EA	0.00	7.00	0.00	28.00
579. Clean cabinetry - lower - inside and out	29.33 LF	0.00	16.46	0.00	482.77
580. Clean cabinetry - upper - inside and out	8.00 LF	0.00	16.46	0.00	131.68
581. Clean countertop	58.67 SF	0.00	0.82	0.00	48.11
582. Clean sink	2.00 EA	0.00	14.53	0.00	29.06
583. Clean sink faucet	2.00 EA	0.00	10.81	0.00	21.62
584. Clean cove base molding - rubber or vinyl	37.38 LF	0.00	0.38	0.00	14.20
Totals: Kitchen				0.00	1,230.16



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190



Room 112

Height: 10'

1,007.25 SF Walls	1,054.66 SF Ceiling
2,061.91 SF Walls & Ceiling	1,009.44 SF Floor
112.16 SY Flooring	100.00 LF Floor Perimeter
132.00 LF Ceil. Perimeter	

Door	2' 6" X 6' 8"	Opens into HALLWAY
Door	3' X 6' 8"	Opens into STORAGE_ARE2
Window	2' 6" X 3' 6"	Opens into STORAGE_ARE2
Window	2' 10" X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
585. Remove Suspended ceiling tile - 2' x 4'	1,054.66 SF	0.29	0.00	0.00	305.85
586. Clean more than the walls	2,014.50 SF	0.00	0.40	0.00	805.80
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
587. Clean light fixture - fluorescent	40.00 EA	0.00	15.75	0.00	630.00
588. Clean floor	2,018.89 SF	0.00	0.46	0.00	928.69
589. Clean window unit (per side) 10 - 20 SF	18.00 EA	0.00	16.86	0.00	303.48
590. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
591. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
592. Clean baseboard	200.00 LF	0.00	0.40	0.00	80.00
593. Clean door / window opening (per side)	22.00 EA	0.00	14.53	0.00	319.66
594. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker, emergency light and alarm sensor	3.00 HR	0.00	47.11	0.00	141.33
595. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
596. Clean outlet or switch	20.00 EA	0.00	3.88	0.00	77.60
597. Clean smoke/carbon monoxide detector	4.00 EA	0.00	7.00	0.00	28.00




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 112

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
598. Clean cabinetry - lower - inside and out	49.33 LF	0.00	16.46	0.00	811.97
599. Clean countertop	90.44 SF	0.00	0.82	0.00	74.16
600. Clean sink	2.00 EA	0.00	14.53	0.00	29.06
601. Clean sink faucet	2.00 EA	0.00	10.81	0.00	21.62
602. Clean bookcase	48.00 SF	0.00	1.25	0.00	60.00
603. Clean thermostat	1.00 EA	0.00	14.29	0.00	14.29
604. Clean radiator unit	1.00 EA	0.00	39.36	0.00	39.36
605. Clean cove base molding - rubber or vinyl	200.00 LF	0.00	0.38	0.00	76.00
606. Clean suspended ceiling grid	1,054.66 SF	0.00	0.34	0.00	358.58
Totals: Room 112				0.00	5,176.09



Room 111

Height: 10'

947.38 SF Walls	908.77 SF Ceiling
1,856.15 SF Walls & Ceiling	854.06 SF Floor
94.90 SY Flooring	87.00 LF Floor Perimeter
121.43 LF Ceil. Perimeter	

Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Door	3' 1" X 6' 8"	Opens into HALLWAY

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
607. Remove Suspended ceiling tile - 2' x 4'	908.77 SF	0.29	0.00	0.00	263.54
608. Clean more than the walls cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning	1,894.77 SF	0.00	0.40	0.00	757.91
609. Clean light fixture - fluorescent	40.00 EA	0.00	15.75	0.00	630.00
610. Clean floor	1,708.12 SF	0.00	0.46	0.00	785.74



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190


CONTINUED - Room 111

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
611. Clean window unit (per side) 10 - 20 SF	16.00 EA	0.00	16.86	0.00	269.76
612. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
613. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
614. Clean baseboard	173.99 LF	0.00	0.40	0.00	69.60
615. Clean door / window opening (per side)	18.00 EA	0.00	14.53	0.00	261.54
616. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker, and locker	3.00 HR	0.00	47.11	0.00	141.33
617. Clean phone, TV, or speaker outlet	20.00 EA	0.00	2.96	0.00	59.20
618. Clean outlet or switch	46.00 EA	0.00	3.88	0.00	178.48
619. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
620. Clean sink	2.00 EA	0.00	14.53	0.00	29.06
621. Clean sink faucet	2.00 EA	0.00	10.81	0.00	21.62
622. Clean cabinetry - lower - inside and out	54.67 LF	0.00	16.46	0.00	899.87
623. Clean countertop	109.33 SF	0.00	0.82	0.00	89.65
624. Clean cove base molding - rubber or vinyl	173.99 LF	0.00	0.38	0.00	66.12
625. Clean suspended ceiling grid	908.77 SF	0.00	0.34	0.00	308.98
Totals: Room 111				0.00	4,898.24



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190



Room 110

Height: 10'

953.29 SF Walls	915.77 SF Ceiling
1,869.05 SF Walls & Ceiling	861.73 SF Floor
95.75 SY Flooring	87.84 LF Floor Perimeter
121.94 LF Ceil. Perimeter	

Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Door	3' 1" X 6' 8"	Opens into HALLWAY

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
626. Remove Suspended ceiling tile - 2' x 4'	915.77 SF	0.29	0.00	0.00	265.57
627. Clean more than the walls	1,906.58 SF	0.00	0.40	0.00	762.63
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
628. Clean light fixture - fluorescent	40.00 EA	0.00	15.75	0.00	630.00
629. Clean floor	1,723.45 SF	0.00	0.46	0.00	792.79
630. Clean window unit (per side) 10 - 20 SF	16.00 EA	0.00	16.86	0.00	269.76
631. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
632. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
633. Clean baseboard	175.67 LF	0.00	0.40	0.00	70.27
634. Clean door / window opening (per side)	18.00 EA	0.00	14.53	0.00	261.54
635. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker, and locker	3.00 HR	0.00	47.11	0.00	141.33
636. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
637. Clean outlet or switch	40.00 EA	0.00	3.88	0.00	155.20
638. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
639. Clean sink	2.00 EA	0.00	14.53	0.00	29.06
640. Clean sink faucet	2.00 EA	0.00	10.81	0.00	21.62




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 110

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
641. Clean cabinetry - lower - inside and out	54.00 LF	0.00	16.46	0.00	888.84
642. Clean countertop	108.00 SF	0.00	0.82	0.00	88.56
643. Clean cove base molding - rubber or vinyl	175.67 LF	0.00	0.38	0.00	66.75
644. Clean suspended ceiling grid	915.77 SF	0.00	0.34	0.00	311.36
Totals: Room 110				0.00	4,844.80



Room 109

Height: 10'

951.34 SF Walls	910.90 SF Ceiling
1,862.24 SF Walls & Ceiling	856.90 SF Floor
95.21 SY Flooring	87.75 LF Floor Perimeter
121.67 LF Ceil. Perimeter	

Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Door	3' X 6' 8"	Opens into HALLWAY

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
645. Remove Suspended ceiling tile - 2' x 4'	910.90 SF	0.29	0.00	0.00	264.16
646. Clean more than the walls	1,902.67 SF	0.00	0.40	0.00	761.07
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
647. Clean light fixture - fluorescent	40.00 EA	0.00	15.75	0.00	630.00
648. Clean floor	1,713.81 SF	0.00	0.46	0.00	788.35
649. Clean window unit (per side) 10 - 20 SF	16.00 EA	0.00	16.86	0.00	269.76
650. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
651. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
652. Clean baseboard	175.51 LF	0.00	0.40	0.00	70.20




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 109

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
653. Clean door / window opening (per side)	18.00 EA	0.00	14.53	0.00	261.54
654. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker, and locker	3.00 HR	0.00	47.11	0.00	141.33
655. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
656. Clean outlet or switch	40.00 EA	0.00	3.88	0.00	155.20
657. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
658. Clean sink	2.00 EA	0.00	14.53	0.00	29.06
659. Clean sink faucet	2.00 EA	0.00	10.81	0.00	21.62
660. Clean cabinetry - lower - inside and out	54.00 LF	0.00	16.46	0.00	888.84
661. Clean countertop	108.00 SF	0.00	0.82	0.00	88.56
662. Clean cove base molding - rubber or vinyl	175.51 LF	0.00	0.38	0.00	66.69
663. Clean suspended ceiling grid	910.90 SF	0.00	0.34	0.00	309.71
Totals: Room 109				0.00	4,835.61



Room 108

Height: 10'

955.36 SF Walls	916.44 SF Ceiling
1,871.81 SF Walls & Ceiling	862.61 SF Floor
95.85 SY Flooring	88.48 LF Floor Perimeter
122.00 LF Ceil. Perimeter	

Door	3' 1" X 6' 8"	Opens into HALLWAY
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
664. Remove Suspended ceiling tile - 2' x 4'	916.44 SF	0.29	0.00	0.00	265.77



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 108

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
665. Clean more than the walls cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning	1,910.73 SF	0.00	0.40	0.00	764.29
666. Clean light fixture - fluorescent	40.00 EA	0.00	15.75	0.00	630.00
667. Clean floor	1,725.22 SF	0.00	0.46	0.00	793.60
668. Clean window unit (per side) 10 - 20 SF	16.00 EA	0.00	16.86	0.00	269.76
669. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
670. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
671. Clean baseboard	176.97 LF	0.00	0.40	0.00	70.79
672. Clean door / window opening (per side)	18.00 EA	0.00	14.53	0.00	261.54
673. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker, and locker	3.00 HR	0.00	47.11	0.00	141.33
674. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
675. Clean outlet or switch	40.00 EA	0.00	3.88	0.00	155.20
676. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
677. Clean cabinetry - lower - inside and out	53.83 LF	0.00	16.46	0.00	886.04
678. Clean countertop	107.67 SF	0.00	0.82	0.00	88.29
679. Clean cove base molding - rubber or vinyl	176.97 LF	0.00	0.38	0.00	67.25
680. Clean suspended ceiling grid	916.44 SF	0.00	0.34	0.00	311.59
Totals: Room 108				0.00	4,794.97



Girls Bathroom

Height: 9' 3"

875.76 SF Walls	399.84 SF Ceiling
1,275.60 SF Walls & Ceiling	398.66 SF Floor
44.30 SY Flooring	95.84 LF Floor Perimeter
91.67 LF Ceil. Perimeter	

Door 2' 6" X 6' 8"
Missing Wall - Goes to Ceiling 3' 4" X 2' 7"

Opens into ROOM13
Opens into GIRLS_BATHRO

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
681. Remove Suspended ceiling tile - 2' x 4'	399.84 SF	0.29	0.00	0.00	115.95



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

CONTINUED - Girls Bathroom

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
682. Clean more than the walls	1,751.52 SF	0.00	0.40	0.00	700.61
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
683. Clean light fixture - fluorescent	16.00 EA	0.00	15.75	0.00	252.00
684. Clean floor - tile	797.32 SF	0.00	0.64	0.00	510.28
685. Clean window unit (per side) 10 - 20 SF	2.00 EA	0.00	16.86	0.00	33.72
686. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
687. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
688. Clean baseboard	191.68 LF	0.00	0.40	0.00	76.67
689. Clean door / window opening (per side)	4.00 EA	0.00	14.53	0.00	58.12
690. Cleaning Technician - incl. cleaning agent - per hour	3.00 HR	0.00	47.11	0.00	141.33
to clean fire/speaker, emergency lights, and paper towel dispensers					
691. Clean toilet partition - per stall	12.00 EA	0.00	29.49	0.00	353.88
692. Clean toilet	12.00 EA	0.00	24.42	0.00	293.04
693. Clean toilet seat	12.00 EA	0.00	5.27	0.00	63.24
694. Clean sink	12.00 EA	0.00	14.53	0.00	174.36
695. Clean sink faucet	10.00 EA	0.00	10.81	0.00	108.10
696. Clean radiator unit	2.00 EA	0.00	39.36	0.00	78.72
697. Clean soap/hand sanitizer dispenser	2.00 EA	0.00	7.90	0.00	15.80
698. Clean toilet paper dispenser	12.00 EA	0.00	7.88	0.00	94.56
699. Clean evaporative cooler diffuser	4.00 EA	0.00	17.47	0.00	69.88
700. Clean cove base molding - rubber or vinyl	191.68 LF	0.00	0.38	0.00	72.84
701. Clean suspended ceiling grid	399.84 SF	0.00	0.34	0.00	135.95
Totals: Girls Bathroom				0.00	3,379.95




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Entry/Foyer

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
714. Clean phone, TV, or speaker outlet	2.00 EA	0.00	2.96	0.00	5.92
715. Clean smoke/carbon monoxide detector	4.00 EA	0.00	7.00	0.00	28.00
716. Clean thermostat	2.00 EA	0.00	14.29	0.00	28.58
717. Clean cove base molding - rubber or vinyl	195.45 LF	0.00	0.38	0.00	74.27
718. Clean suspended ceiling grid	942.75 SF	0.00	0.34	0.00	320.54
Totals: Entry/Foyer				0.00	3,298.75



Men's Room

Height: 14' 2"

603.03 SF Walls	62.87 SF Ceiling
665.90 SF Walls & Ceiling	62.87 SF Floor
6.99 SY Flooring	41.24 LF Floor Perimeter
43.74 LF Ceil. Perimeter	

Door	2' 6" X 6' 8"	Opens into Exterior			
DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
719. Remove Suspended ceiling tile - 2' x 4'	62.87 SF	0.29	0.00	0.00	18.23
720. Clean more than the walls	1,206.06 SF	0.00	0.40	0.00	482.42
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
721. Clean light fixture - fluorescent	14.00 EA	0.00	15.75	0.00	220.50
722. Clean light fixture - fluorescent	14.00 EA	0.00	15.75	0.00	220.50
723. Additional cost for high wall or ceiling - 11' to 14'	293.38 SF	0.00	0.05	0.00	14.67
724. Clean floor	125.74 SF	0.00	0.46	0.00	57.84
725. Clean window unit (per side) 10 - 20 SF	18.00 EA	0.00	16.86	0.00	303.48
726. Clean door (per side)	12.00 EA	0.00	8.03	0.00	96.36
727. Clean door hardware	10.00 EA	0.00	7.42	0.00	74.20
728. Clean baseboard	82.49 LF	0.00	0.40	0.00	33.00
729. Clean door / window opening (per side)	22.00 EA	0.00	14.53	0.00	319.66
730. Clean door / window opening (per side)	LF	0.00	0.86	0.00	0.00
731. Cleaning Technician - incl. cleaning agent - per hour	1.00 HR	0.00	47.11	0.00	47.11



Valcon Contracting Corp.


185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Men's Room

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
to clean PA speaker					
732. Clean phone, TV, or speaker outlet	4.00 EA	0.00	2.96	0.00	11.84
733. Clean outlet or switch	40.00 EA	0.00	3.88	0.00	155.20
734. Clean smoke/carbon monoxide detector	4.00 EA	0.00	7.00	0.00	28.00
735. Clean cove base molding - rubber or vinyl	82.49 LF	0.00	0.38	0.00	31.35
736. Clean suspended ceiling grid	62.87 SF	0.00	0.34	0.00	21.38
Totals: Men's Room				0.00	2,135.74


Asst. Principal

Height: 14' 2"



1,286.78 SF Walls	403.64 SF Ceiling
1,690.42 SF Walls & Ceiling	403.64 SF Floor
44.85 SY Flooring	94.11 LF Floor Perimeter
99.11 LF Ceil. Perimeter	

Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Door	2' 6" X 6' 8"	Opens into Exterior



Subroom: Restroom (1)

Height: 14' 2"

209.47 SF Walls	13.83 SF Ceiling
223.30 SF Walls & Ceiling	13.83 SF Floor
1.54 SY Flooring	13.46 LF Floor Perimeter
15.96 LF Ceil. Perimeter	

Door	2' 6" X 6' 8"	Opens into ASST_PRINCI
-------------	----------------------	-------------------------------

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
737. Clean more than the walls	2,992.50 SF	0.00	0.40	0.00	1,197.00
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
738. Clean light fixture - fluorescent	10.00 EA	0.00	15.75	0.00	157.50
739. Clean light fixture	2.00 EA	0.00	11.85	0.00	23.70




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Asst. Principal

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
740. Clean floor	834.94 SF	0.00	0.46	0.00	384.07
741. Clean window unit (per side) 10 - 20 SF	8.00 EA	0.00	16.86	0.00	134.88
742. Clean door (per side)	6.00 EA	0.00	8.03	0.00	48.18
743. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68
744. Clean baseboard	215.15 LF	0.00	0.40	0.00	86.06
745. Clean door / window opening (per side)	32.00 EA	0.00	14.53	0.00	464.96
746. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker, emergency light and paper towel dispenser	1.00 HR	0.00	47.11	0.00	47.11
747. Clean phone, TV, or speaker outlet	2.00 EA	0.00	2.96	0.00	5.92
748. Clean outlet or switch	12.00 EA	0.00	3.88	0.00	46.56
749. Clean smoke/carbon monoxide detector	4.00 EA	0.00	7.00	0.00	28.00
750. Clean radiator cover	6.00 EA	0.00	13.53	0.00	81.18
751. Clean cold air return cover	2.00 EA	0.00	9.73	0.00	19.46
752. Clean toilet	2.00 EA	0.00	24.42	0.00	48.84
753. Clean toilet seat	2.00 EA	0.00	5.27	0.00	10.54
754. Clean sink	2.00 EA	0.00	14.53	0.00	29.06
755. Clean sink faucet	2.00 EA	0.00	10.81	0.00	21.62
756. Clean soap/hand sanitizer dispenser	2.00 EA	0.00	7.90	0.00	15.80
757. Clean toilet paper dispenser	2.00 EA	0.00	7.88	0.00	15.76
758. Clean cove base molding - rubber or vinyl	215.15 LF	0.00	0.38	0.00	81.76
759. Clean suspended ceiling grid	417.47 SF	0.00	0.34	0.00	141.94
Totals: Asst. Principal				0.00	3,119.58



Stairs

Height: 26' 2"

599.05 SF Walls
 682.19 SF Walls & Ceiling
 15.55 SY Flooring
 27.50 LF Ceil. Perimeter


83.14 SF Ceiling
 139.94 SF Floor
 31.85 LF Floor Perimeter



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs



Subroom: Room22 (4)


Height: 13' 5"

503.48 SF Walls	94.83 SF Ceiling
598.31 SF Walls & Ceiling	94.83 SF Floor
10.54 SY Flooring	34.25 LF Floor Perimeter
34.25 LF Ceil. Perimeter	

Missing Wall

6' 5" X 13' 5"

Opens into STAIRS3



Subroom: Room1 (3)


Height: 13' 5"

450.58 SF Walls	89.96 SF Ceiling
540.54 SF Walls & Ceiling	89.96 SF Floor
10.00 SY Flooring	33.58 LF Floor Perimeter
33.58 LF Ceil. Perimeter	

Missing Wall

6' 1" X 13' 5"

Opens into STAIRS

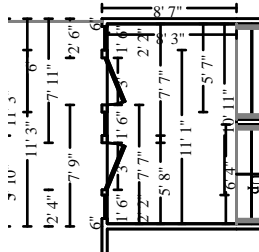

Subroom: Stairs1 (2)

Height: 17' 5"

508.36 SF Walls	105.19 SF Ceiling
613.55 SF Walls & Ceiling	105.19 SF Floor
11.69 SY Flooring	29.25 LF Floor Perimeter
29.25 LF Ceil. Perimeter	

Missing Wall

6' 1" X 17' 4 9/16"

Opens into STAIRS

Window

1' 6" X 4'

Opens into ENTRY_FOYER

Door

3' X 6' 8"

Opens into ENTRY_FOYER

Window

1' 6" X 4'

Opens into ENTRY_FOYER

Door

3' X 6' 8"

Opens into ENTRY_FOYER

Window

1' 6" X 4'

Opens into ENTRY_FOYER

Missing Wall

6' 4" X 17' 4 9/16"


Opens into STAIRS2



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs



Subroom: Stairs2 (1)

Height: 17' 5"


380.89 SF Walls	85.50 SF Ceiling
466.39 SF Walls & Ceiling	152.56 SF Floor
16.95 SY Flooring	39.16 LF Floor Perimeter
33.33 LF Ceil. Perimeter	

Missing Wall

6' 4" X 17' 4 9/16"

Opens into STAIRS1

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
760. Clean more than the walls	4,884.73 SF	0.00	0.40	0.00	1,953.89
761. Additional cost for high wall or ceiling - 11' to 14'	473.34 SF	0.00	0.05	0.00	23.67
762. Clean balustrade	15.42 LF	0.00	2.93	0.00	45.18
763. Clean stair riser - per side - per LF	380.00 LF	0.00	0.62	0.00	235.60
764. Clean stair tread - per side - per LF	354.67 LF	0.00	0.73	0.00	258.91
765. Clean light fixture - fluorescent	4.00 EA	0.00	15.75	0.00	63.00
766. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
767. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68
768. Clean window unit (per side) 3 - 9 SF	6.00 EA	0.00	11.80	0.00	70.80
769. Clean window unit (per side) 10 - 20 SF	6.00 EA	0.00	16.86	0.00	101.16
770. Clean handrail - wall mounted	46.25 LF	0.00	0.58	0.00	26.83
771. Cleaning Technician - incl. cleaning agent - per hour to clean exit signs	1.00 HR	0.00	47.11	0.00	47.11
772. Clean floor	105.19 SF	0.00	0.46	0.00	48.39
Totals: Stairs				0.00	2,936.34



Stairs3

Height: 27' 5"

709.61 SF Walls	101.06 SF Ceiling
810.68 SF Walls & Ceiling	169.01 SF Floor
18.78 SY Flooring	36.62 LF Floor Perimeter
31.67 LF Ceil. Perimeter	

Missing Wall

6' 5" X 27' 4 5/8"


Opens into ROOM22



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs3




Subroom: Stairs1 (2)

Height: 17' 5"

624.23 SF Walls	149.37 SF Ceiling
773.60 SF Walls & Ceiling	149.37 SF Floor
16.60 SY Flooring	35.92 LF Floor Perimeter
35.92 LF Ceil. Perimeter	

Missing Wall	6' 5" X 17' 4 9/16"	Opens into STAIRS3
Window	1' 6" X 4'	Opens into HALLWAY
Door	3' 6" X 6' 8"	Opens into HALLWAY
Window	1' 6" X 4'	Opens into HALLWAY
Door	3' 6" X 6' 8"	Opens into HALLWAY
Window	1' 6" X 4'	Opens into HALLWAY
Missing Wall	6' 4" X 17' 4 9/16"	Opens into STAIRS4



Subroom: Stairs2 (1)

Height: 17' 5"

388.62 SF Walls	98.69 SF Ceiling
487.31 SF Walls & Ceiling	167.60 SF Floor
18.62 SY Flooring	36.09 LF Floor Perimeter
31.17 LF Ceil. Perimeter	

Missing Wall	6' 4" X 17' 4 9/16"	Opens into STAIRS5
--------------	---------------------	--------------------

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
773. Clean more than the walls	3,444.92 SF	0.00	0.40	0.00	1,377.97
774. Additional cost for high wall or ceiling - 11' to 14'	754.21 SF	0.00	0.05	0.00	37.71
775. Clean balustrade	15.42 LF	0.00	2.93	0.00	45.18
776. Clean stair riser - per side - per LF	367.33 LF	0.00	0.62	0.00	227.74
777. Clean stair tread - per side - per LF	342.00 LF	0.00	0.73	0.00	249.66
778. Clean light fixture - fluorescent	4.00 EA	0.00	15.75	0.00	63.00
779. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
780. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68
781. Clean window unit (per side) 3 - 9 SF	6.00 EA	0.00	11.80	0.00	70.80
782. Clean window unit (per side) 10 - 20 SF	6.00 EA	0.00	16.86	0.00	101.16
783. Clean handrail - wall mounted	46.25 LF	0.00	0.58	0.00	26.83



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs3

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
784. Cleaning Technician - incl. cleaning agent - per hour to clean exit signs	1.00 HR	0.00	47.11	0.00	47.11
785. Clean floor	167.60 SF	0.00	0.46	0.00	77.10
Totals: Stairs3				0.00	2,386.06
Total: Main Level				0.00	79,491.20

Level 2

Level 2

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
786. Clean cove base molding - rubber or vinyl	LF	0.00	0.38	0.00	0.00
Total: Level 2				0.00	0.00

Hallway

Height: 10'


	2,105.55 SF Walls	1,623.95 SF Ceiling
	3,729.50 SF Walls & Ceiling	1,407.94 SF Floor
	156.44 SY Flooring	252.49 LF Floor Perimeter
	288.74 LF Ceil. Perimeter	
Door	3' X 6' 8"	Opens into Exterior
Door	3' X 6' 8"	Opens into ROOM_214
Door	3' X 6' 8"	Opens into Exterior
Door	3' X 6' 8"	Opens into Exterior
Window	1' 6" X 4'	Opens into STAIRS5
Door	3' 6" X 6' 8"	Opens into STAIRS5
Window	1' 6" X 4'	Opens into STAIRS5
Door	3' 6" X 6' 8"	Opens into STAIRS5
Window	1' 6" X 4'	Opens into STAIRS5
Door	3' X 6' 8"	Opens into Exterior
Door	3' X 6' 8"	Opens into Exterior
Door	3' X 6' 8"	Opens into Exterior
Door	3' X 6' 8"	Opens into Exterior



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Hallway



Subroom: Closet (2)


Height: 10'

349.94 SF Walls	81.04 SF Ceiling
430.98 SF Walls & Ceiling	81.04 SF Floor
9.00 SY Flooring	34.16 LF Floor Perimeter
36.66 LF Ceil. Perimeter	

Door

2' 6" X 6' 8"

Opens into ROOM13



Subroom: Room13 (1)

Height: 10'

1,045.07 SF Walls	740.13 SF Ceiling
1,785.19 SF Walls & Ceiling	740.13 SF Floor
82.24 SY Flooring	96.84 LF Floor Perimeter
119.84 LF Ceil. Perimeter	

Door

5' 3" X 6' 8"

Opens into HALLWAY

Door

2' 6" X 6' 8"

Opens into Exterior

Door

2' 6" X 6' 8"

Opens into Exterior

Missing Wall

10' 9 5/16" X 10'

Opens into Exterior

Door

2' 6" X 6' 8"

Opens into ASST_PRINCI

Door

2' 6" X 6' 8"

Opens into CLOSET

Door

5' 3" X 6' 8"

Opens into Exterior

Door

2' 6" X 6' 8"

Opens into Exterior

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
787. Remove Suspended ceiling tile - 2' x 4'	2,445.11 SF	0.29	0.00	0.00	709.08
788. Clean more than the walls	7,001.11 SF	0.00	0.40	0.00	2,800.44
cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning					
789. Cleaning Technician - incl. cleaning agent - per hour	288.00 HR	0.00	47.11	0.00	13,567.68
6 workers 8 hours each for 3 days. To clean the 264 lockers inside and outside					
790. Clean light fixture - fluorescent	38.00 EA	0.00	15.75	0.00	598.50
791. Clean floor	4,458.20 SF	0.00	0.46	0.00	2,050.77
792. Clean door (per side)	40.00 EA	0.00	8.03	0.00	321.20
793. Clean door hardware	40.00 EA	0.00	7.42	0.00	296.80
794. Clean baseboard	766.99 LF	0.00	0.40	0.00	306.80
795. Clean door / window opening (per side)	40.00 EA	0.00	14.53	0.00	581.20




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 213


DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
806. Clean window unit (per side) 10 - 20 SF	18.00 EA	0.00	16.86	0.00	303.48
807. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
808. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68
809. Clean baseboard	182.63 LF	0.00	0.40	0.00	73.05
810. Clean door / window opening (per side)	22.00 EA	0.00	14.53	0.00	319.66
811. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker, emergency light, locker and alarm sensor	3.00 HR	0.00	47.11	0.00	141.33
812. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
813. Clean outlet or switch	20.00 EA	0.00	3.88	0.00	77.60
814. Clean evaporative cooler diffuser	2.00 EA	0.00	17.47	0.00	34.94
815. Clean cabinetry - lower - inside and out	64.67 LF	0.00	16.46	0.00	1,064.47
816. Clean countertop	129.33 SF	0.00	0.82	0.00	106.05
817. Clean suspended ceiling grid	1,097.33 SF	0.00	0.34	0.00	373.09
Totals: Room 213				0.00	5,304.71



Stairs

Height: 26' 2"

599.05 SF Walls	103.64 SF Ceiling
702.69 SF Walls & Ceiling	174.45 SF Floor
19.38 SY Flooring	31.85 LF Floor Perimeter
27.50 LF Ceil. Perimeter	



Subroom: Room1 (3)

Height: 13' 5"

470.70 SF Walls	100.71 SF Ceiling
571.41 SF Walls & Ceiling	100.71 SF Floor
11.19 SY Flooring	35.08 LF Floor Perimeter
35.08 LF Ceil. Perimeter	

Missing Wall

7' 7" X 13' 5"


Opens into STAIRS



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs




Subroom: Stairs1 (2)

Height: 17' 5"

531.54 SF Walls	116.37 SF Ceiling
647.91 SF Walls & Ceiling	116.37 SF Floor
12.93 SY Flooring	30.58 LF Floor Perimeter
30.58 LF Ceil. Perimeter	

Missing Wall	7' 7" X 17' 4 9/16"	Opens into STAIRS
Door	2' 6" X 6' 8"	Opens into Exterior
Door	2' 6" X 6' 8"	Opens into Exterior
Missing Wall	6' 4" X 17' 4 9/16"	Opens into STAIRS2



Subroom: Stairs2 (1)

Height: 17' 5"

380.89 SF Walls	85.50 SF Ceiling
466.39 SF Walls & Ceiling	152.56 SF Floor
16.95 SY Flooring	39.16 LF Floor Perimeter
33.33 LF Ceil. Perimeter	

Missing Wall	6' 4" X 17' 4 9/16"	Opens into STAIRS1
---------------------	----------------------------	---------------------------

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
818. Clean the walls - Heavy	1,982.18 SF	0.00	0.50	0.00	991.09
819. Clean the walls	1,982.18 SF	0.00	0.40	0.00	792.87
820. Additional cost for high wall or ceiling - 11' to 14'	523.69 SF	0.00	0.05	0.00	26.18
821. Clean balustrade - Heavy	15.42 LF	0.00	4.18	0.00	64.46
822. Clean balustrade	15.42 LF	0.00	2.93	0.00	45.18
823. Clean stair riser - per side - per LF	380.00 LF	0.00	0.62	0.00	235.60
824. Clean stair tread - per side - per LF	354.67 LF	0.00	0.73	0.00	258.91
825. Clean light fixture - fluorescent	4.00 EA	0.00	15.75	0.00	63.00
826. Clean door - with detail (per side)	4.00 EA	0.00	12.00	0.00	48.00
827. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
828. Clean door hardware - Heavy	4.00 EA	0.00	10.38	0.00	41.52
829. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68
830. Clean window unit (per side) 3 - 9 SF - Heavy	6.00 EA	0.00	16.57	0.00	99.42




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs


DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
831. Clean window unit (per side) 3 - 9 SF	6.00 EA	0.00	11.80	0.00	70.80
832. Clean window unit (per side) 10 - 20 SF - Heavy	6.00 EA	0.00	23.69	0.00	142.14
833. Clean window unit (per side) 10 - 20 SF	6.00 EA	0.00	16.86	0.00	101.16
834. Clean handrail - wall mounted - Heavy	46.25 LF	0.00	0.85	0.00	39.31
835. Clean handrail - wall mounted	46.25 LF	0.00	0.58	0.00	26.83
836. Cleaning Technician - incl. cleaning agent - per hour to clean exit signs	1.00 HR	0.00	47.11	0.00	47.11
837. Clean floor - Heavy	116.37 SF	0.00	0.66	0.00	76.80
838. Clean floor	116.37 SF	0.00	0.46	0.00	53.53
839. Clean cove base molding - rubber or vinyl	136.68 LF	0.00	0.38	0.00	51.94
Totals: Stairs				0.00	3,337.65



Stairs3

Height: 27' 5"

709.61 SF Walls	105.00 SF Ceiling
814.61 SF Walls & Ceiling	175.59 SF Floor
19.51 SY Flooring	36.62 LF Floor Perimeter
31.67 LF Ceil. Perimeter	



Subroom: Room22 (3)

Height: 13' 5"

520.21 SF Walls	100.19 SF Ceiling
620.41 SF Walls & Ceiling	100.19 SF Floor
11.13 SY Flooring	35.33 LF Floor Perimeter
35.33 LF Ceil. Perimeter	

Missing Wall

6' 8" X 13' 5"


Opens into STAIRS3



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs3

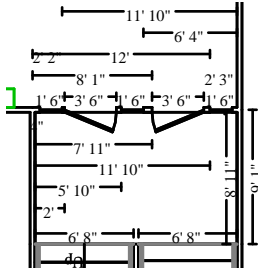


Subroom: Stairs1 (2)

Height: 17' 5"

547.47 SF Walls	121.86 SF Ceiling
669.33 SF Walls & Ceiling	121.86 SF Floor
13.54 SY Flooring	31.50 LF Floor Perimeter
31.50 LF Ceil. Perimeter	

Missing Wall	6' 8" X 17' 4 9/16"	Opens into STAIRS3
Window	1' 6" X 4'	Opens into HALLWAY
Door	3' 6" X 6' 8"	Opens into HALLWAY
Window	1' 6" X 4'	Opens into HALLWAY
Door	3' 6" X 6' 8"	Opens into HALLWAY
Window	1' 6" X 4'	Opens into HALLWAY
Missing Wall	6' 8" X 17' 4 9/16"	Opens into STAIRS4



Subroom: Stairs2 (1)

Height: 17' 5"

388.62 SF Walls	103.89 SF Ceiling
492.51 SF Walls & Ceiling	176.42 SF Floor
19.60 SY Flooring	36.09 LF Floor Perimeter
31.17 LF Ceil. Perimeter	

Missing Wall	6' 8" X 17' 4 9/16"	Opens into STAIRS5
--------------	---------------------	--------------------

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
840. Clean the walls - Heavy	2,165.91 SF	0.00	0.50	0.00	1,082.96
841. Clean the walls	2,165.91 SF	0.00	0.40	0.00	866.36
842. Additional cost for high wall or ceiling - 11' to 14'	793.91 SF	0.00	0.05	0.00	39.70
843. Clean balustrade - Heavy	15.42 LF	0.00	4.18	0.00	64.46
844. Clean balustrade	15.42 LF	0.00	2.93	0.00	45.18
845. Clean stair riser - per side - per LF	367.33 LF	0.00	0.62	0.00	227.74
846. Clean stair tread - per side - per LF	342.00 LF	0.00	0.73	0.00	249.66
847. Clean light fixture - fluorescent	4.00 EA	0.00	15.75	0.00	63.00
848. Clean door - with detail (per side)	4.00 EA	0.00	12.00	0.00	48.00
849. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
850. Clean door hardware - Heavy	4.00 EA	0.00	10.38	0.00	41.52
851. Clean door hardware	4.00 EA	0.00	7.42	0.00	29.68




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Stairs3

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
852. Clean window unit (per side) 3 - 9 SF - Heavy	6.00 EA	0.00	16.57	0.00	99.42
853. Clean window unit (per side) 3 - 9 SF	6.00 EA	0.00	11.80	0.00	70.80
854. Clean window unit (per side) 10 - 20 SF - Heavy	6.00 EA	0.00	23.69	0.00	142.14
855. Clean window unit (per side) 10 - 20 SF	6.00 EA	0.00	16.86	0.00	101.16
856. Clean handrail - wall mounted - Heavy	46.25 LF	0.00	0.85	0.00	39.31
857. Clean handrail - wall mounted	46.25 LF	0.00	0.58	0.00	26.83
858. Cleaning Technician - incl. cleaning agent - per hour to clean exit signs	1.00 HR	0.00	47.11	0.00	47.11
859. Clean floor - Heavy	176.42 SF	0.00	0.66	0.00	116.44
860. Clean floor	176.42 SF	0.00	0.46	0.00	81.15
861. Clean cove base molding - rubber or vinyl	139.54 LF	0.00	0.38	0.00	53.03
Totals: Stairs3				0.00	3,567.77

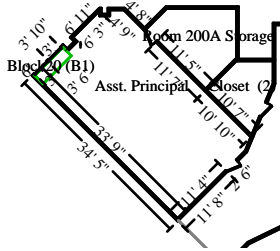

Asst. Principal

Height: 10'

949.06 SF Walls	606.32 SF Ceiling
1,555.38 SF Walls & Ceiling	593.15 SF Floor
65.91 SY Flooring	90.70 LF Floor Perimeter
105.33 LF Ceil. Perimeter	

Door	2' 6" X 6' 8"	Opens into ROOM_200A_ST
Window	3' X 7'	Opens into Exterior
Window	3' X 7'	Opens into Exterior
Door	2' 6" X 6' 8"	Opens into ROOM13

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
862. Remove Suspended ceiling tile - 2' x 4'	606.32 SF	0.29	0.00	0.00	175.83
863. Clean more than the walls cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning	1,898.13 SF	0.00	0.40	0.00	759.25
864. Clean light fixture - fluorescent	24.00 EA	0.00	15.75	0.00	378.00
865. Clean floor	1,186.31 SF	0.00	0.46	0.00	545.70




Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Asst. Principal

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
866. Clean window unit (per side) 10 - 20 SF	4.00 EA	0.00	16.86	0.00	67.44
867. Clean door (per side)	4.00 EA	0.00	8.03	0.00	32.12
868. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
869. Clean baseboard	181.40 LF	0.00	0.40	0.00	72.56
870. Clean door / window opening (per side)	8.00 EA	0.00	14.53	0.00	116.24
871. Clean radiator cover	2.00 EA	0.00	13.53	0.00	27.06
872. Cleaning Technician - incl. cleaning agent - per hour to clean PA speaker, fire strobe/speaker, locker and alarm sensor	3.00 HR	0.00	47.11	0.00	141.33
873. Clean phone, TV, or speaker outlet	8.00 EA	0.00	2.96	0.00	23.68
874. Clean outlet or switch	20.00 EA	0.00	3.88	0.00	77.60
875. Clean cabinetry - lower - inside and out	13.33 LF	0.00	16.46	0.00	219.41
876. Clean countertop	26.67 SF	0.00	0.82	0.00	21.87
877. Clean cove base molding - rubber or vinyl	181.40 LF	0.00	0.38	0.00	68.93
878. Clean suspended ceiling grid	606.32 SF	0.00	0.34	0.00	206.15
Totals: Asst. Principal				0.00	2,948.01

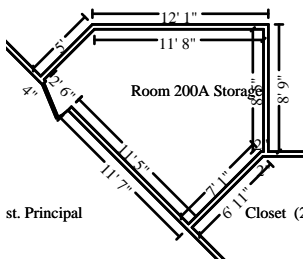

Room 200A Storage

Height: 10'

445.89 SF Walls	133.80 SF Ceiling
579.69 SF Walls & Ceiling	133.80 SF Floor
14.87 SY Flooring	43.76 LF Floor Perimeter
46.26 LF Ceil. Perimeter	

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
879. Remove Suspended ceiling tile - 2' x 4'	133.80 SF	0.29	0.00	0.00	38.80
880. Clean more than the walls cleaned a 2nd. time after suspended ceiling installed and the room was full of dust. School officials demanded the 2nd. cleaning	891.78 SF	0.00	0.40	0.00	356.71
881. Clean light fixture - fluorescent	7.00 EA	0.00	15.75	0.00	110.25
882. Clean light fixture	2.00 EA	0.00	11.85	0.00	23.70
883. Clean floor	267.61 SF	0.00	0.46	0.00	123.10

CROSS_HILL

12/9/2021

Page: 66



Valcon Contracting Corp.

185 Summerfield Street
 Scarsdale, NY 10583
 Tel: 718-652-0190

CONTINUED - Room 200A Storage

DESCRIPTION	QTY	REMOVE	REPLACE	TAX	TOTAL
884. Clean door (per side)	2.00 EA	0.00	8.03	0.00	16.06
885. Clean door hardware	2.00 EA	0.00	7.42	0.00	14.84
886. Clean baseboard	87.51 LF	0.00	0.40	0.00	35.00
887. Clean door / window opening (per side)	22.00 EA	0.00	14.53	0.00	319.66
888. Clean phone, TV, or speaker outlet	4.00 EA	0.00	2.96	0.00	11.84
889. Clean outlet or switch	4.00 EA	0.00	3.88	0.00	15.52
890. Clean smoke/carbon monoxide detector	2.00 EA	0.00	7.00	0.00	14.00
891. Clean cove base molding - rubber or vinyl	87.51 LF	0.00	0.38	0.00	33.25
892. Clean suspended ceiling grid	133.80 SF	0.00	0.34	0.00	45.49
Totals: Room 200A Storage				0.00	1,158.22
Total: Level 2				0.00	39,255.29
Line Item Totals: CROSS_HILL				0.00	235,195.60

Grand Total Areas:

53,828.76 SF Walls	28,441.16 SF Ceiling	82,269.91 SF Walls and Ceiling
28,327.25 SF Floor	3,147.47 SY Flooring	4,530.06 LF Floor Perimeter
0.00 SF Long Wall	0.00 SF Short Wall	5,172.69 LF Ceil. Perimeter
28,327.25 Floor Area	29,865.29 Total Area	44,230.15 Interior Wall Area
20,643.68 Exterior Wall Area	1,978.57 Exterior Perimeter of Walls	
0.00 Surface Area	0.00 Number of Squares	0.00 Total Perimeter Length
0.00 Total Ridge Length	0.00 Total Hip Length	



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

Summary for Dwelling

Line Item Total	235,195.60
Replacement Cost Value	\$235,195.60
Net Claim	\$235,195.60

Damian Reyes



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

Recap of Taxes



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

Recap by Room

Estimate: CROSS_HILL	35,960.57	15.29%
Area: Basement		
Classroom 1	7,084.99	3.01%
Classroom 2 & 2A	6,385.74	2.72%
Classroom 2B	3,731.26	1.59%
Classroom 3A	2,775.68	1.18%
Storage Area/Room	1,172.33	0.50%
Office 3B	1,105.46	0.47%
Office 3C	1,349.81	0.57%
Classroom 4	6,213.46	2.64%
Stock 4B	755.35	0.32%
Storage 4A	1,240.37	0.53%
Office 4C	1,422.30	0.60%
Classroom 5	5,253.35	2.23%
Storage 5A	1,010.01	0.43%
Classroom 6	20,326.39	8.64%
Classroom 7	5,335.66	2.27%
Storage 7A	940.70	0.40%
Storage 7B	700.31	0.30%
Office 7C	827.05	0.35%
Hallway	6,881.37	2.93%
Stairs	3,077.04	1.31%
Stairs3	2,899.91	1.23%
<hr/>		
Area Subtotal: Basement	80,488.54	34.22%
Area: Main Level		
Hallway	21,166.09	9.00%
Room 114	4,842.32	2.06%
Room 114A	3,157.02	1.34%
Room 113	5,068.73	2.16%
Storage Area/Room	2,220.75	0.94%
Kitchen	1,230.16	0.52%
Room 112	5,176.09	2.20%
Room 111	4,898.24	2.08%
Room 110	4,844.80	2.06%
Room 109	4,835.61	2.06%
Room 108	4,794.97	2.04%
Girls Bathroom	3,379.95	1.44%
Entry/Foyer	3,298.75	1.40%
Men's Room	2,135.74	0.91%
Asst. Principal	3,119.58	1.33%
Stairs	2,936.34	1.25%
Stairs3	2,386.06	1.01%



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

Area Subtotal: Main Level	79,491.20	33.80%
Area: Level 2		
Hallway	22,938.93	9.75%
Room 213	5,304.71	2.26%
Stairs	3,337.65	1.42%
Stairs3	3,567.77	1.52%
Asst. Principal	2,948.01	1.25%
Room 200A Storage	1,158.22	0.49%
<hr/>	<hr/>	<hr/>
Area Subtotal: Level 2	39,255.29	16.69%
<hr/>	<hr/>	<hr/>
Subtotal of Areas	235,195.60	100.00%
<hr/>	<hr/>	<hr/>
Total	235,195.60	100.00%



Valcon Contracting Corp.

185 Summerfield Street
Scarsdale, NY 10583
Tel: 718-652-0190

Recap by Category

Items	Total	%
CLEANING	175,095.25	74.45%
GENERAL DEMOLITION	18,615.07	7.91%
FRAMING & ROUGH CARPENTRY	266.65	0.11%
HAZARDOUS MATERIAL REMEDIATION	20,681.88	8.79%
LABOR ONLY	10,395.08	4.42%
PAINTING	3,300.73	1.40%
WATER EXTRACTION & REMEDIATION	6,840.94	2.91%
Subtotal	235,195.60	100.00%

